


SCHMIDT 3RD FLOOR RENOVATION - CONSTRUCTION SCHEDULE - REVISED 9-12-12

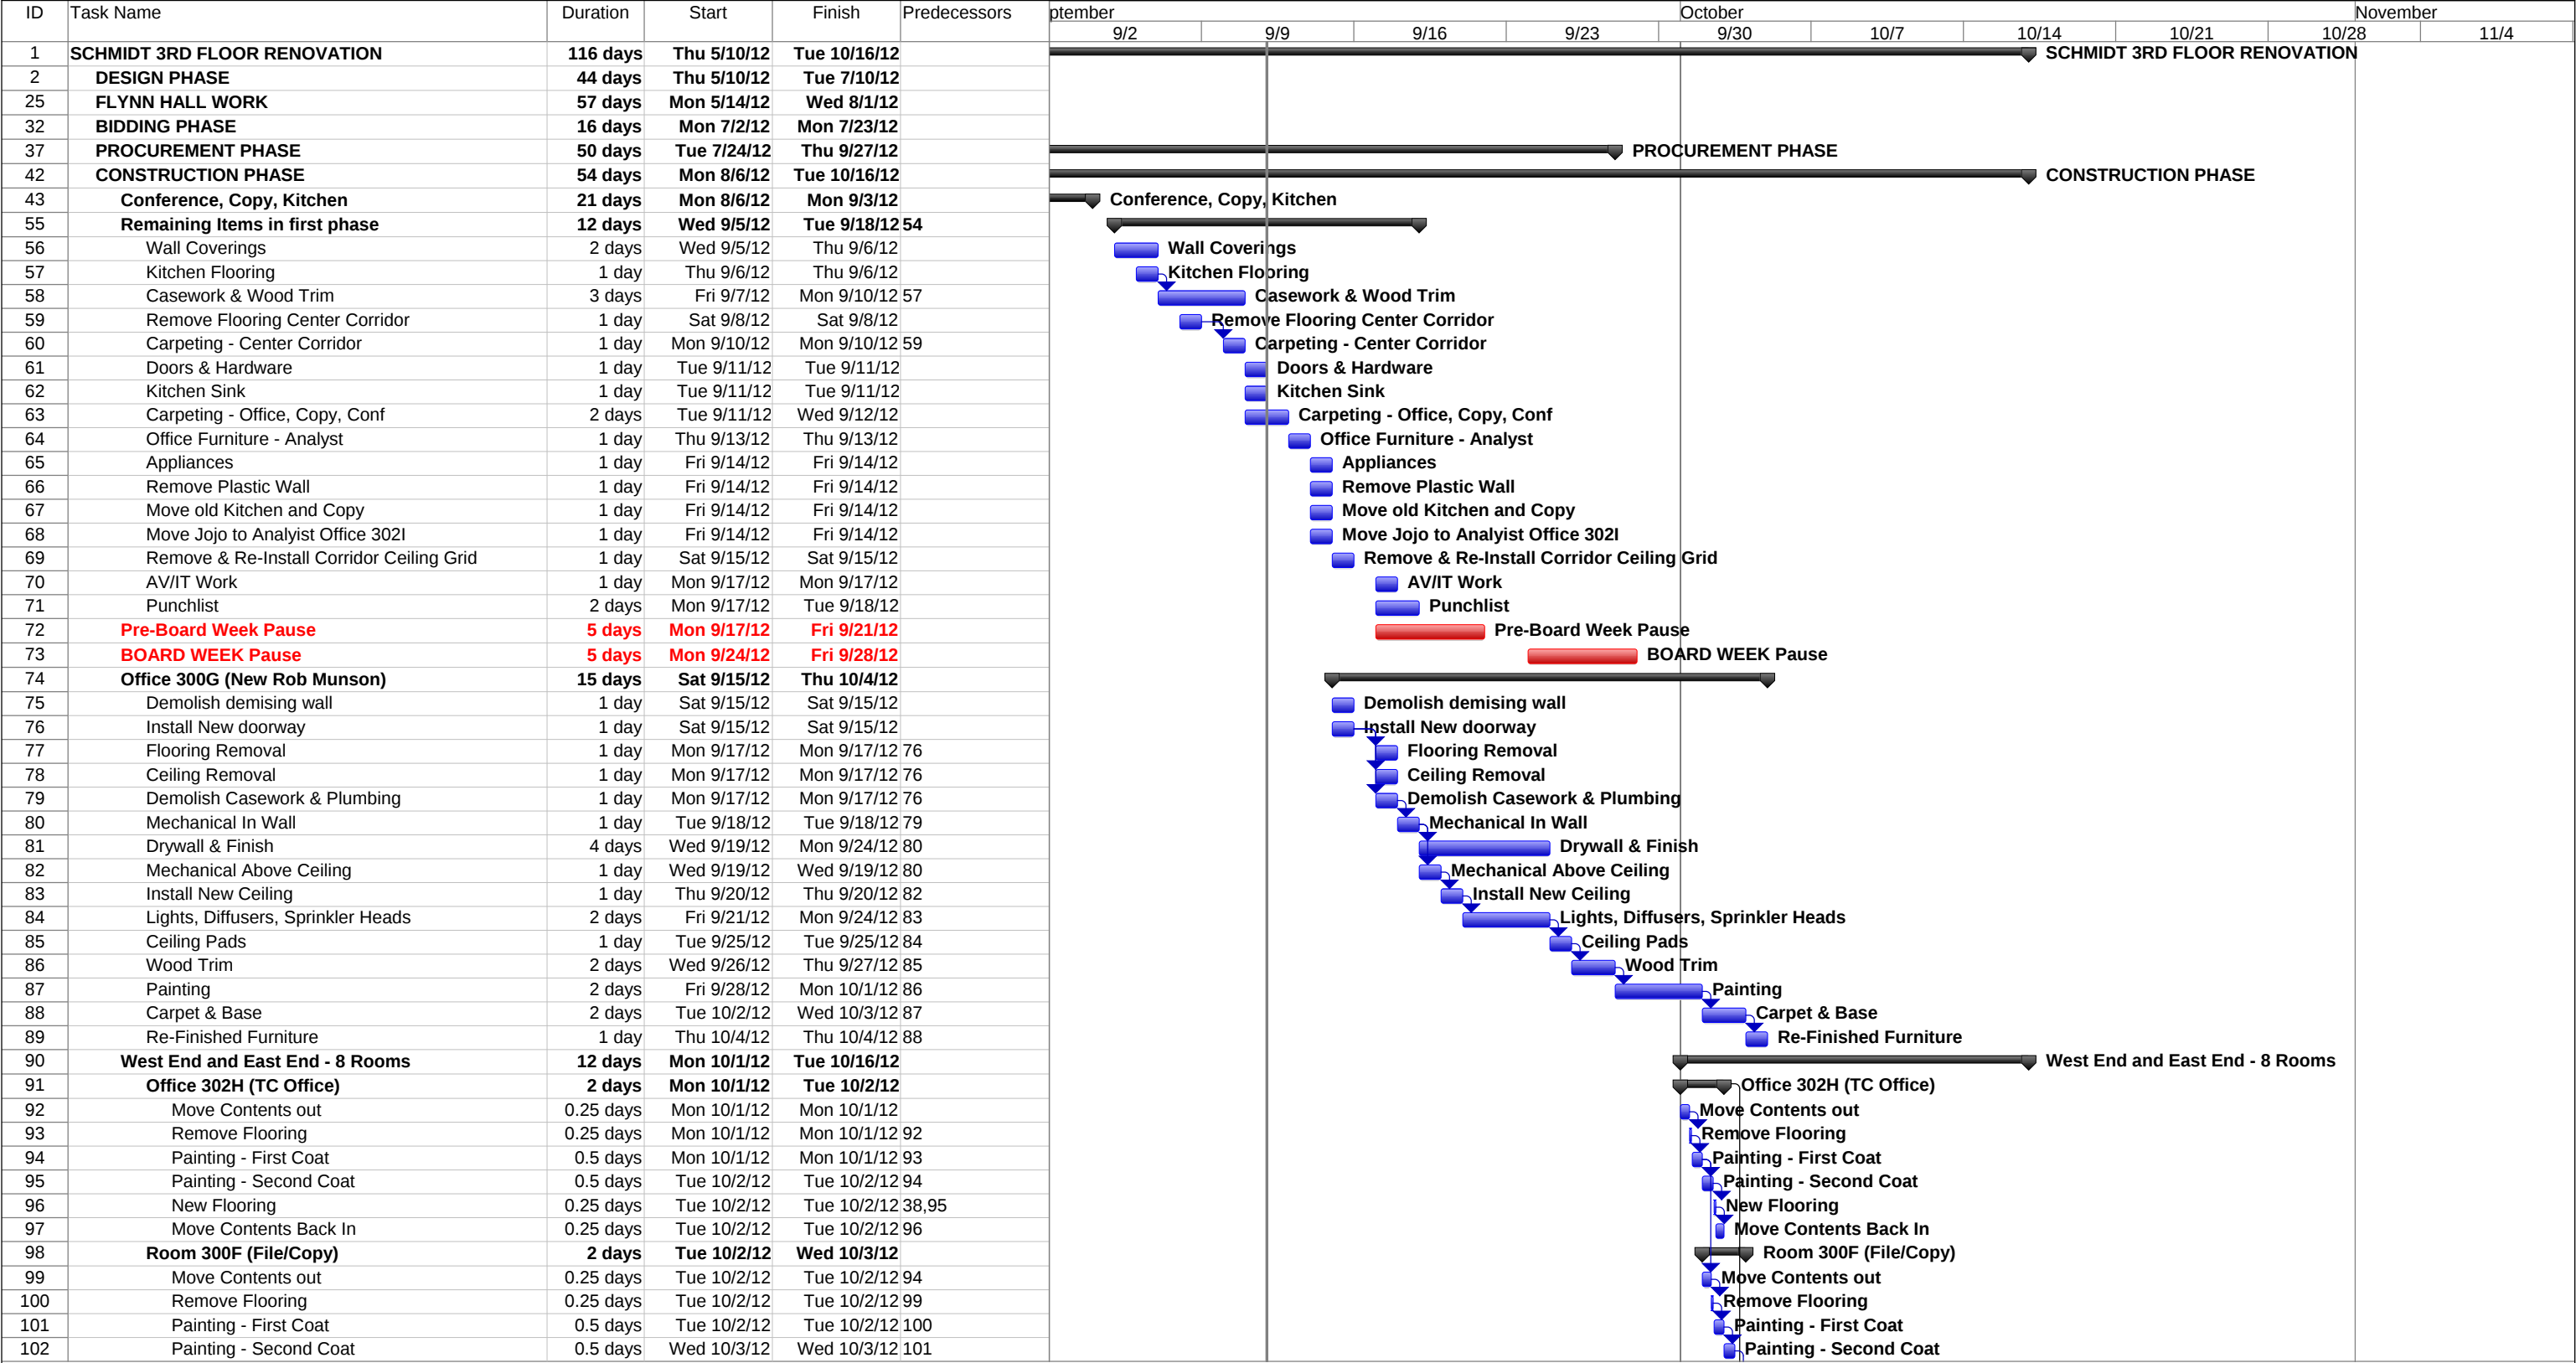

Project: Schmidt 3RD Floor Reno Sche
Date: Wed 9/12/12
By: Joe Frecker, XU Const. Mgr.

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Progress

Deadline

SCHMIDT 3RD FLOOR RENOVATION - CONSTRUCTION SCHEDULE - REVISED 9-12-12

ID	Task Name	Duration	Start	Finish	Predecessors	September				October				November	
						9/2	9/9	9/16	9/23	9/30	10/7	10/14	10/21	10/28	11/4
103	New Flooring	0.25 days	Wed 10/3/12	Wed 10/3/12	102						New Flooring				
104	Move Contents Back In	0.25 days	Wed 10/3/12	Wed 10/3/12	103						Move Contents Back In				
105	Office 302G (Shawn Shuler)	2 days	Wed 10/3/12	Thu 10/4/12							Office 302G (Shawn Shuler)				
106	Move Contents out	0.25 days	Wed 10/3/12	Wed 10/3/12	91						Move Contents out				
107	Remove Flooring	0.25 days	Wed 10/3/12	Wed 10/3/12	106						Remove Flooring				
108	Painting - First Coat	0.5 days	Wed 10/3/12	Wed 10/3/12	107						Painting - First Coat				
109	Painting - Second Coat	0.5 days	Thu 10/4/12	Thu 10/4/12	108						Painting - Second Coat				
110	New Flooring	0.25 days	Thu 10/4/12	Thu 10/4/12	109						New Flooring				
111	Move Contents Back In	0.25 days	Thu 10/4/12	Thu 10/4/12	110						Move Contents Back In				
112	Office 300E (Connie Panko)	2 days	Mon 10/8/12	Tue 10/9/12							Office 300E (Connie Panko)				
113	Move Contents out	0.25 days	Mon 10/8/12	Mon 10/8/12	105FS+1 day						Move Contents out				
114	Remove Flooring	0.25 days	Mon 10/8/12	Mon 10/8/12	113						Remove Flooring				
115	Painting - First Coat	0.5 days	Mon 10/8/12	Mon 10/8/12	114						Painting - First Coat				
116	Painting - Second Coat	0.5 days	Tue 10/9/12	Tue 10/9/12	115						Painting - Second Coat				
117	New Flooring	0.25 days	Tue 10/9/12	Tue 10/9/12	116						New Flooring				
118	Move Contents Back In	0.25 days	Tue 10/9/12	Tue 10/9/12	117						Move Contents Back In				
119	Office 302E (Current Rob Munson)	2 days	Tue 10/9/12	Wed 10/10/12							Office 302E (Current Rob Munson)				
120	Move Contents out	0.25 days	Tue 10/9/12	Tue 10/9/12	115						Move Contents out				
121	Remove Flooring	0.25 days	Tue 10/9/12	Tue 10/9/12	120						Remove Flooring				
122	Painting - First Coat	0.5 days	Tue 10/9/12	Tue 10/9/12	121						Painting - First Coat				
123	Painting - Second Coat	0.5 days	Wed 10/10/12	Wed 10/10/12	122						Painting - Second Coat				
124	New Flooring	0.25 days	Wed 10/10/12	Wed 10/10/12	123						New Flooring				
125	Move Contents Back In	0.25 days	Wed 10/10/12	Wed 10/10/12	124						Move Contents Back In				
126	Office 300D (Beth Amyot)	2 days	Wed 10/10/12	Thu 10/11/12							Office 300D (Beth Amyot)				
127	Move Contents out	0.25 days	Wed 10/10/12	Wed 10/10/12	112						Move Contents out				
128	Remove Flooring	0.25 days	Wed 10/10/12	Wed 10/10/12	127						Remove Flooring				
129	Painting - 1st Coat & WallCovering	0.5 days	Wed 10/10/12	Wed 10/10/12	128						Painting - 1st Coat & WallCovering				
130	Painting - 2nd Coat & WallCovering	0.5 days	Thu 10/11/12	Thu 10/11/12	129						Painting - 2nd Coat & WallCovering				
131	New Flooring	0.25 days	Thu 10/11/12	Thu 10/11/12	130						New Flooring				
132	Move Contents Back In	0.25 days	Thu 10/11/12	Thu 10/11/12	131						Move Contents Back In				
133	Office 300A & 300H (Judy Janzen)	2 days	Thu 10/11/12	Fri 10/12/12							Office 300A & 300H (Judy Janzen)				
134	Move Contents out	0.25 days	Thu 10/11/12	Thu 10/11/12	119						Move Contents out				
135	Remove Flooring	0.25 days	Thu 10/11/12	Thu 10/11/12	134						Remove Flooring				
136	Painting - 1st Coat & WallCovering	0.5 days	Thu 10/11/12	Thu 10/11/12	135						Painting - 1st Coat & WallCovering				
137	Painting - 2nd Coat & WallCovering	0.5 days	Fri 10/12/12	Fri 10/12/12	136						Painting - 2nd Coat & WallCovering				
138	New Flooring	0.25 days	Fri 10/12/12	Fri 10/12/12	137						New Flooring				
139	Move Contents Back In	0.25 days	Fri 10/12/12	Fri 10/12/12	138						Move Contents Back In				
140	Conference Room Table	1 day	Mon 10/15/12	Mon 10/15/12							Conference Room Table				
141	Punchlist	2 days	Mon 10/15/12	Tue 10/16/12	139						Punchlist				

Project: Schmidt 3RD Floor Reno Sche
Date: Wed 9/12/12
By: Joe Frecker, XU Const. Mgr.

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Progress

Deadline
