


KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March		
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16
1	KUHLMAN RENOVATION SCHEDULE	156 days	Wed 1/1/14	Fri 8/8/14													
2	Design	53 days	Wed 1/1/14	Fri 3/14/14													
3	Permit	15 days	Mon 3/17/14	Fri 4/4/14	2												
4	Bid Period	15 days	Mon 3/17/14	Fri 4/4/14	2												
5	Pre-Bid Walk Thru	1 day	Mon 3/24/14	Mon 3/24/14													
6	Bids Due	1 day	Fri 4/4/14	Fri 4/4/14	4FF												
7	Award	5 days	Mon 4/7/14	Fri 4/11/14	6												
8	Material Lead Time	20 days	Mon 4/14/14	Fri 5/9/14	7												
9	Construction	144 days	Wed 1/1/14	Tue 7/22/14													
10	Secure Construction Site / Install barricades and signage	2 days	Mon 5/12/14	Tue 5/13/14	8												
11	HVAC System Shutdown	15 days	Wed 5/14/14	Tue 6/3/14													
12	New Fan Coil Valves	15 days	Wed 5/14/14	Tue 6/3/14	10												
13	Air / Dirt Separator	3 days	Fri 5/30/14	Tue 6/3/14	12FF												
14	SIXTH FLOOR	23 days	Wed 5/14/14	Fri 6/13/14													
15	DORM ROOMS/BATHROOMS	23 days	Wed 5/14/14	Fri 6/13/14													
16	Replace UV with Fan Coil Unit	4 days	Wed 5/28/14	Mon 6/2/14	10FS+10 days												
17	Replace Vanities	4 days	Wed 5/14/14	Mon 5/19/14	10												
18	Repairs to wardrobes	3 days	Tue 5/20/14	Thu 5/22/14	17												
19	Sink Plumbing	2 days	Mon 5/19/14	Tue 5/20/14	17FS-1 day												
20	Replace bathrm exhaust grills	1 day	Fri 5/23/14	Fri 5/23/14	18												
21	Toilet Room Accessories	2 days	Mon 5/26/14	Tue 5/27/14	20												
22	Misc repairs to finishes	1 day	Wed 5/28/14	Wed 5/28/14	21												
23	Replace Acoustic Ceilings	4 days	Thu 5/29/14	Tue 6/3/14	22												
24	Lighting	4 days	Wed 6/4/14	Mon 6/9/14	23												
25	Field Certify HM Frames	2 days	Tue 6/10/14	Wed 6/11/14	24												
26	New Dorm Room Doors	2 days	Tue 6/10/14	Wed 6/11/14	24												
27	Card Access Hardware	2 days	Thu 6/12/14	Fri 6/13/14	26												
28	Painting	4 days	Tue 6/10/14	Fri 6/13/14	24												
29	FLOOR LOUNGE	9 days	Thu 5/29/14	Tue 6/10/14													
30	Remove Ceiling	1 day	Thu 5/29/14	Thu 5/29/14	22												
31	Casework/Sink	1 day	Fri 5/30/14	Fri 5/30/14	30												
32	Fan Coil Unit	1 day	Tue 6/3/14	Tue 6/3/14	31,16												
33	Replace Ceiling	1 day	Wed 6/4/14	Wed 6/4/14	32												
34	Lighting/Sensors/Grills	1 day	Thu 6/5/14	Thu 6/5/14	33												
35	Painting	1 day	Fri 6/6/14	Fri 6/6/14	34												
36	Flooring	1 day	Mon 6/9/14	Mon 6/9/14	35												
37	Furniture	1 day	Tue 6/10/14	Tue 6/10/14	36												
38	CORRIDORS	6 days	Mon 6/2/14	Mon 6/9/14													
39	Drinking Fountain	1 day	Mon 6/2/14	Mon 6/2/14	31												

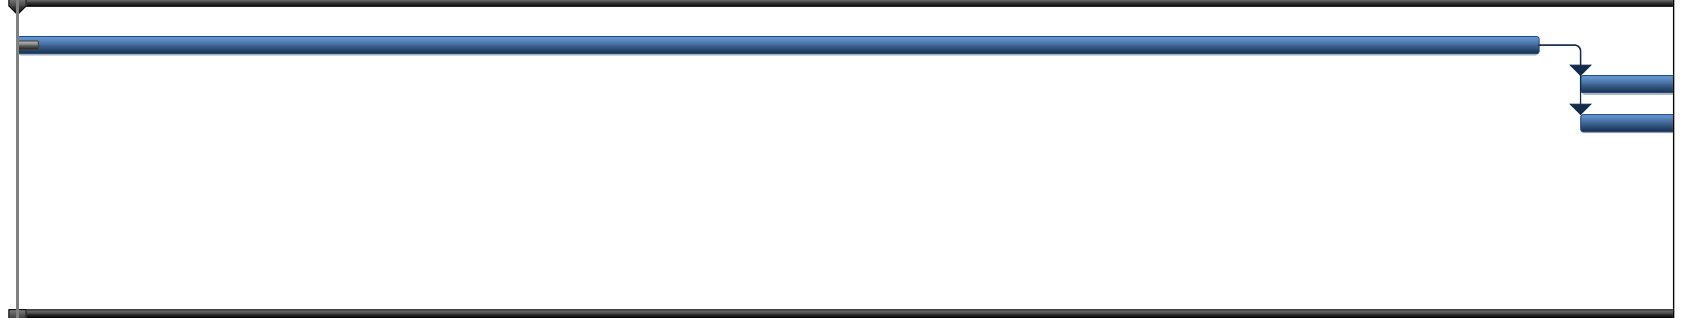

Project: Kuhlman Architectural Re
Date: 3/14/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March			
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16	
40	Isolation Valves	1 day	Tue 6/3/14	Tue 6/3/14	39													
41	Bulletin Boards	1 day	Thu 6/5/14	Thu 6/5/14	40													
42	Painting	2 days	Wed 6/4/14	Thu 6/5/14	40													
43	Flooring	2 days	Fri 6/6/14	Mon 6/9/14	42													
44	LOBBY	7 days	Wed 6/4/14	Thu 6/12/14														
45	Fan Coil Unit	1 day	Wed 6/4/14	Wed 6/4/14	32													
46	Doors / Hold Opens	1 day	Thu 6/5/14	Thu 6/5/14	45													
47	Drinking Fountain	1 day	Fri 6/6/14	Fri 6/6/14	46													
48	Painting	1 day	Mon 6/9/14	Mon 6/9/14	47													
49	Flooring	3 days	Tue 6/10/14	Thu 6/12/14	48													
50	FIFTH FLOOR	22 days	Tue 5/20/14	Wed 6/18/14														
51	DORM ROOMS/BATHROOMS	16 days	Tue 5/20/14	Tue 6/10/14														
52	Replace UV with Fan Coil Unit	4 days	Tue 6/3/14	Fri 6/6/14	16													
53	Replace Vanities	4 days	Tue 5/20/14	Fri 5/23/14	17													
54	Repairs to wardrobes	3 days	Fri 5/23/14	Tue 5/27/14	18													
55	Sink Plumbing	2 days	Fri 5/23/14	Mon 5/26/14	53FS-1 day													
56	Replace bathrm exhaust grills	1 day	Mon 5/26/14	Mon 5/26/14	20													
57	Toilet Room Accessories	2 days	Tue 5/27/14	Wed 5/28/14	56													
58	Misc repairs to finishes	1 day	Thu 5/29/14	Thu 5/29/14	57													
59	Lighting	4 days	Fri 5/30/14	Wed 6/4/14	58													
60	Field Certify HM Frames	2 days	Thu 6/5/14	Fri 6/6/14	59													
61	New Dorm Room Doors	2 days	Thu 6/5/14	Fri 6/6/14	59													
62	Card Access Hardware	2 days	Mon 6/9/14	Tue 6/10/14	61													
63	Painting	4 days	Thu 6/5/14	Tue 6/10/14	59													
64	FLOOR LOUNGE	8 days	Thu 6/5/14	Mon 6/16/14														
65	Remove Ceiling	1 day	Thu 6/5/14	Thu 6/5/14	59													
66	Casework/Sink	1 day	Fri 6/6/14	Fri 6/6/14	65													
67	Fan Coil Unit	1 day	Mon 6/9/14	Mon 6/9/14	66,52													
68	Replace Ceiling	1 day	Tue 6/10/14	Tue 6/10/14	67													
69	Lighting/Sensors/Grills	1 day	Wed 6/11/14	Wed 6/11/14	68													
70	Painting	1 day	Thu 6/12/14	Thu 6/12/14	69													
71	Flooring	1 day	Fri 6/13/14	Fri 6/13/14	70													
72	Furniture	1 day	Mon 6/16/14	Mon 6/16/14	71													
73	CORRIDORS	6 days	Mon 6/9/14	Mon 6/16/14														
74	Drinking Fountain	1 day	Mon 6/9/14	Mon 6/9/14	66													
75	Bulletin Boards	1 day	Tue 6/10/14	Tue 6/10/14	74													
76	Painting	2 days	Wed 6/11/14	Thu 6/12/14	75													
77	Flooring	2 days	Fri 6/13/14	Mon 6/16/14	76													
78	LOBBY	7 days	Tue 6/10/14	Wed 6/18/14														

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March			
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16	
79	Fan Coil Unit	1 day	Tue 6/10/14	Tue 6/10/14	67													
80	Doors / Hold Opens	1 day	Wed 6/11/14	Wed 6/11/14	79													
81	Drinking Fountain	1 day	Thu 6/12/14	Thu 6/12/14	80													
82	Painting	1 day	Fri 6/13/14	Fri 6/13/14	81													
83	Flooring	3 days	Mon 6/16/14	Wed 6/18/14	82													
84	FOURTH FLOOR	22 days	Mon 5/26/14	Tue 6/24/14														
85	DORM ROOMS/BATHROOMS	16 days	Mon 5/26/14	Mon 6/16/14														
86	Replace UV with Fan Coil Unit	4 days	Mon 6/9/14	Thu 6/12/14	52													
87	Replace Vanities	4 days	Mon 5/26/14	Thu 5/29/14	53													
88	Repairs to wardrobes	3 days	Fri 5/30/14	Tue 6/3/14	87													
89	Sink Plumbing	2 days	Thu 5/29/14	Fri 5/30/14	87FS-1 day													
90	Replace bathrm exhaust grills	1 day	Fri 5/30/14	Fri 5/30/14	87													
91	Toilet Room Accessories	2 days	Mon 6/2/14	Tue 6/3/14	90													
92	Misc repairs to finishes	1 day	Wed 6/4/14	Wed 6/4/14	91													
93	Lighting	4 days	Thu 6/5/14	Tue 6/10/14	92													
94	Field Certify HM Frames	2 days	Wed 6/11/14	Thu 6/12/14	93													
95	New Dorm Room Doors	2 days	Wed 6/11/14	Thu 6/12/14	93													
96	Card Access Hardware	2 days	Fri 6/13/14	Mon 6/16/14	95													
97	Painting	4 days	Wed 6/11/14	Mon 6/16/14	93													
98	FLOOR LOUNGE	8 days	Wed 6/11/14	Fri 6/20/14														
99	Remove Ceiling	1 day	Wed 6/11/14	Wed 6/11/14	93													
100	Casework/Sink	1 day	Thu 6/12/14	Thu 6/12/14	99													
101	Fan Coil Unit	1 day	Fri 6/13/14	Fri 6/13/14	100,86													
102	Replace Ceiling	1 day	Mon 6/16/14	Mon 6/16/14	101													
103	Lighting/Sensors/Grills	1 day	Tue 6/17/14	Tue 6/17/14	102													
104	Painting	1 day	Wed 6/18/14	Wed 6/18/14	103													
105	Flooring	1 day	Thu 6/19/14	Thu 6/19/14	104													
106	Furniture	1 day	Fri 6/20/14	Fri 6/20/14	105													
107	CORRIDORS	6 days	Fri 6/13/14	Fri 6/20/14														
108	Drinking Fountain	1 day	Fri 6/13/14	Fri 6/13/14	100													
109	Bulletin Boards	1 day	Mon 6/16/14	Mon 6/16/14	108													
110	Painting	2 days	Tue 6/17/14	Wed 6/18/14	109													
111	Flooring	2 days	Thu 6/19/14	Fri 6/20/14	110													
112	LOBBY	7 days	Mon 6/16/14	Tue 6/24/14														
113	Fan Coil Unit	1 day	Mon 6/16/14	Mon 6/16/14	101													
114	Doors / Hold Opens	1 day	Tue 6/17/14	Tue 6/17/14	113													
115	Drinking Fountain	1 day	Wed 6/18/14	Wed 6/18/14	114													
116	Painting	1 day	Thu 6/19/14	Thu 6/19/14	115													
117	Flooring	3 days	Fri 6/20/14	Tue 6/24/14	116													

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March		
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16
118	THIRD FLOOR	23 days	Fri 5/30/14	Tue 7/1/14													
119	DORM ROOMS/BATHROOMS	16 days	Fri 5/30/14	Fri 6/20/14													
120	Replace UV with Fan Coil Unit	4 days	Fri 6/13/14	Wed 6/18/14	86												
121	Replace Vanities	4 days	Fri 5/30/14	Wed 6/4/14	87												
122	Repairs to wardrobes	3 days	Thu 6/5/14	Mon 6/9/14	121												
123	Sink Plumbing	2 days	Wed 6/4/14	Thu 6/5/14	121FS-1 day												
124	Replace bathrm exhaust grills	1 day	Thu 6/5/14	Thu 6/5/14	121												
125	Toilet Room Accessories	2 days	Fri 6/6/14	Mon 6/9/14	124												
126	Misc repairs to finishes	1 day	Tue 6/10/14	Tue 6/10/14	125												
127	Lighting	4 days	Wed 6/11/14	Mon 6/16/14	126												
128	Field Certify HM Frames	2 days	Tue 6/17/14	Wed 6/18/14	127												
129	New Dorm Room Doors	2 days	Tue 6/17/14	Wed 6/18/14	127												
130	Card Access Hardware	2 days	Thu 6/19/14	Fri 6/20/14	129												
131	Painting	4 days	Tue 6/17/14	Fri 6/20/14	127												
132	FLOOR LOUNGE	10 days	Tue 6/17/14	Mon 6/30/14													
133	Remove Ceiling	1 day	Tue 6/17/14	Tue 6/17/14	127												
134	Remove Masonry Wall	1 day	Wed 6/18/14	Wed 6/18/14	133												
135	Casework/Sink	1 day	Thu 6/19/14	Thu 6/19/14	134												
136	Fan Coil Unit	1 day	Fri 6/20/14	Fri 6/20/14	135,120												
137	Replace Ceiling	1 day	Mon 6/23/14	Mon 6/23/14	136												
138	Lighting/Sensors/Grills	1 day	Tue 6/24/14	Tue 6/24/14	137												
139	Painting	1 day	Wed 6/25/14	Wed 6/25/14	138												
140	Flooring	2 days	Thu 6/26/14	Fri 6/27/14	139												
141	Furniture	1 day	Mon 6/30/14	Mon 6/30/14	140												
142	CORRIDORS	6 days	Fri 6/20/14	Fri 6/27/14													
143	Drinking Fountain	1 day	Fri 6/20/14	Fri 6/20/14	135												
144	Bulletin Boards	1 day	Mon 6/23/14	Mon 6/23/14	143												
145	Painting	2 days	Tue 6/24/14	Wed 6/25/14	144												
146	Flooring	2 days	Thu 6/26/14	Fri 6/27/14	145												
147	LOBBY	7 days	Mon 6/23/14	Tue 7/1/14													
148	Fan Coil Unit	1 day	Mon 6/23/14	Mon 6/23/14	136												
149	Doors Hold Opens	1 day	Tue 6/24/14	Tue 6/24/14	148												
150	Drinking Fountain	1 day	Wed 6/25/14	Wed 6/25/14	149												
151	Painting	1 day	Thu 6/26/14	Thu 6/26/14	150												
152	Flooring	3 days	Fri 6/27/14	Tue 7/1/14	151												
153	SECOND FLOOR	22 days	Tue 6/10/14	Thu 7/10/14													
154	DORM ROOMS/BATHROOMS	16 days	Tue 6/10/14	Tue 7/1/14													
155	Replace UV with Fan Coil Unit	4 days	Thu 6/19/14	Tue 6/24/14	120												
156	Replace Vanities	4 days	Tue 6/10/14	Fri 6/13/14	122												

Project: Kuhlman Architectural Re Date: 3/14/14	Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline
	Split	External Tasks	Inactive Summary	Manual Summary	Progress
	Milestone	External Milestone	Manual Task	Start-only	
	Summary	Inactive Task	Duration-only	Finish-only	

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March		
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16
157	Repairs to wardrobes	3 days	Mon 6/16/14	Wed 6/18/14	156												
158	Sink Plumbing	2 days	Fri 6/13/14	Mon 6/16/14	156FS-1 day												
159	Replace bathrm exhaust grills	1 day	Mon 6/16/14	Mon 6/16/14	156												
160	Toilet Room Accessories	2 days	Tue 6/17/14	Wed 6/18/14	159												
161	Misc repairs to finishes	1 day	Thu 6/19/14	Thu 6/19/14	160												
162	Lighting	4 days	Fri 6/20/14	Wed 6/25/14	161												
163	Field Certify HM Frames	2 days	Thu 6/26/14	Fri 6/27/14	162												
164	New Dorm Room Doors	2 days	Thu 6/26/14	Fri 6/27/14	162												
165	Card Access Hardware	2 days	Mon 6/30/14	Tue 7/1/14	164												
166	Painting	4 days	Thu 6/26/14	Tue 7/1/14	162												
167	FLOOR LOUNGE	8 days	Thu 6/26/14	Tue 7/8/14													
168	Remove Ceiling	1 day	Thu 6/26/14	Thu 6/26/14	162												
169	Casework/Sink	1 day	Fri 6/27/14	Fri 6/27/14	168												
170	Fan Coil Unit	1 day	Mon 6/30/14	Mon 6/30/14	169,155												
171	Replace Ceiling	1 day	Tue 7/1/14	Tue 7/1/14	170												
172	Lighting/Sensors/Grills	1 day	Wed 7/2/14	Wed 7/2/14	171												
173	Painting	1 day	Thu 7/3/14	Thu 7/3/14	172												
174	Flooring	1 day	Mon 7/7/14	Mon 7/7/14	173												
175	Furniture	1 day	Tue 7/8/14	Tue 7/8/14	174												
176	CORRIDORS	6 days	Mon 6/30/14	Tue 7/8/14													
177	Drinking Fountain	1 day	Mon 6/30/14	Mon 6/30/14	169												
178	Bulletin Boards	1 day	Tue 7/1/14	Tue 7/1/14	177												
179	Painting	2 days	Wed 7/2/14	Thu 7/3/14	178												
180	Flooring	2 days	Mon 7/7/14	Tue 7/8/14	179												
181	LOBBY	7 days	Tue 7/1/14	Thu 7/10/14													
182	Fan Coil Unit	1 day	Tue 7/1/14	Tue 7/1/14	170												
183	Doors / Hold Opens	1 day	Wed 7/2/14	Wed 7/2/14	182												
184	Drinking Fountain	1 day	Thu 7/3/14	Thu 7/3/14	183												
185	Painting	1 day	Mon 7/7/14	Mon 7/7/14	184												
186	Flooring	3 days	Tue 7/8/14	Thu 7/10/14	185												
187	FIRST FLOOR	26 days	Mon 6/16/14	Tue 7/22/14													
188	DORM ROOMS/BATHROOMS	16 days	Mon 6/16/14	Tue 7/8/14													
189	Replace UV with Fan Coil Unit	4 days	Wed 6/25/14	Mon 6/30/14	155												
190	Replace Vanities	4 days	Mon 6/16/14	Thu 6/19/14	156												
191	Repairs to wardrobes	3 days	Fri 6/20/14	Tue 6/24/14	190												
192	Sink Plumbing	2 days	Thu 6/19/14	Fri 6/20/14	190FS-1 day												
193	Replace bathrm exhaust grills	1 day	Fri 6/20/14	Fri 6/20/14	190												
194	Toilet Room Accessories	2 days	Mon 6/23/14	Tue 6/24/14	193												
195	Misc repairs to finishes	1 day	Wed 6/25/14	Wed 6/25/14	194												

Project: Kuhlman Architectural Re Date: 3/14/14	Task Project Summary	Inactive Milestone	Inactive Summary	Manual Summary Rollup	Manual Summary	Deadline
	Split External Tasks	Inactive Task	External Milestone	Manual Task	Start-only	Progress
	Milestone External Milestone	Inactive Task	Duration-only	Finish-only	Start-only	Finish-only

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March		
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16
196	Lighting	4 days	Thu 6/26/14	Tue 7/1/14	195												
197	Field Certify HM Frames	2 days	Wed 7/2/14	Thu 7/3/14	196												
198	New Dorm Room Doors	2 days	Wed 7/2/14	Thu 7/3/14	196												
199	Card Access Hardware	2 days	Mon 7/7/14	Tue 7/8/14	198												
200	Painting	4 days	Wed 7/2/14	Tue 7/8/14	196												
201	FLOOR LOUNGE	10 days	Wed 7/2/14	Wed 7/16/14													
202	Remove Ceiling	1 day	Wed 7/2/14	Wed 7/2/14	196												
203	Casework/Sink	1 day	Thu 7/3/14	Thu 7/3/14	202												
204	Fan Coil Units	3 days	Mon 7/7/14	Wed 7/9/14	203,189												
205	Replace Ceiling	1 day	Thu 7/10/14	Thu 7/10/14	204												
206	Lighting/Sensors/Grills	1 day	Fri 7/11/14	Fri 7/11/14	205												
207	Painting	1 day	Mon 7/14/14	Mon 7/14/14	206												
208	Flooring	1 day	Tue 7/15/14	Tue 7/15/14	207												
209	Furniture	1 day	Wed 7/16/14	Wed 7/16/14	208												
210	CORRIDORS	6 days	Mon 7/7/14	Mon 7/14/14													
211	Drinking Fountain	1 day	Mon 7/7/14	Mon 7/7/14	203												
212	Bulletin Boards	1 day	Tue 7/8/14	Tue 7/8/14	211												
213	Painting	2 days	Wed 7/9/14	Thu 7/10/14	212												
214	Flooring	2 days	Fri 7/11/14	Mon 7/14/14	213												
215	LOBBY	9 days	Thu 7/10/14	Tue 7/22/14													
216	Fan Coil Unit	1 day	Thu 7/10/14	Thu 7/10/14	204												
217	Doors / Hold Opens	1 day	Fri 7/11/14	Fri 7/11/14	216												
218	Drinking Fountain	1 day	Mon 7/14/14	Mon 7/14/14	217												
219	Painting	1 day	Tue 7/15/14	Tue 7/15/14	218												
220	Flooring	5 days	Wed 7/16/14	Tue 7/22/14	219												
221	OTHER AREAS	6 days	Wed 7/9/14	Wed 7/16/14													
222	RA Office	6 days	Wed 7/9/14	Wed 7/16/14	188												
223	Remove Ceiling	1 day	Wed 7/9/14	Wed 7/9/14	224FS-2 days												
224	Casework/Sink	1 day	Thu 7/10/14	Thu 7/10/14	225FS-2 days												
225	Fan Coil Unit	1 day	Fri 7/11/14	Fri 7/11/14	216												
226	Replace Ceiling	1 day	Mon 7/14/14	Mon 7/14/14	225												
227	Lighting/Sensors/Grills	1 day	Tue 7/15/14	Tue 7/15/14	226												
228	Painting	1 day	Wed 7/16/14	Wed 7/16/14	227												
229	GROUND FLOOR	141 days	Wed 1/1/14	Thu 7/17/14													
230	DORM ROOMS/BATHROOMS	141 days	Wed 1/1/14	Thu 7/17/14													
231	Replace UV with Fan Coil Unit	4 days	Tue 7/1/14	Mon 7/7/14	189												
232	Replace Vanities	2 days	Fri 6/20/14	Mon 6/23/14	190												
233	Repairs to wardrobes	2 days	Tue 6/24/14	Wed 6/25/14	232												
234	Sink Plumbing	2 days	Mon 6/23/14	Tue 6/24/14	232FS-1 day												

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January					February				March		
						12/29	1/5	1/12	1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16
235	Replace bathrm exhaust grills	1 day	Tue 6/24/14	Tue 6/24/14	232												
236	Toilet Room Accessories	2 days	Wed 6/25/14	Thu 6/26/14	235												
237	Misc repairs to finishes	1 day	Fri 6/27/14	Fri 6/27/14	236												
238	Replace Acoustic Ceilings/Diffusers	4 days	Mon 6/30/14	Thu 7/3/14	237												
239	Lighting	4 days	Mon 7/7/14	Thu 7/10/14	238												
240	Field Certify HM Frames	2 days	Fri 7/11/14	Mon 7/14/14	239												
241	New Dorm Room Doors	1 day	Fri 7/11/14	Fri 7/11/14	239												
242	Card Access Hardware	2 days	Wed 1/1/14	Thu 1/2/14													
243	Painting	4 days	Fri 7/11/14	Wed 7/16/14	239												
244	OTHER AREAS	12 days	Tue 7/1/14	Thu 7/17/14													
245	Rec Room	12 days	Tue 7/1/14	Thu 7/17/14													
246	Block Walls	3 days	Tue 7/1/14	Thu 7/3/14	189												
247	Drywall Ceiling	2 days	Mon 7/7/14	Tue 7/8/14	246												
248	Painting	2 days	Wed 7/9/14	Thu 7/10/14	247												
249	Doors & Hardware	1 day	Fri 7/11/14	Fri 7/11/14	248												
250	Flooring	3 days	Fri 7/11/14	Tue 7/15/14	248												
251	Furniture	2 days	Wed 7/16/14	Thu 7/17/14	250												
252	CORRIDORS	8 days	Wed 6/25/14	Mon 7/7/14													
253	Drinking Fountain	1 day	Wed 6/25/14	Wed 6/25/14	234												
254	Isolation Valves	1 day	Thu 6/26/14	Thu 6/26/14	253												
255	Bulletin Boards	1 day	Fri 6/27/14	Fri 6/27/14	254												
256	Painting	2 days	Mon 6/30/14	Tue 7/1/14	255												
257	Flooring	3 days	Wed 7/2/14	Mon 7/7/14	256												
258	LOBBY	7 days	Tue 7/8/14	Wed 7/16/14													
259	Fan Coil Unit	1 day	Tue 7/8/14	Tue 7/8/14	231												
260	Doors	1 day	Wed 7/9/14	Wed 7/9/14	259												
261	Drinking Fountain	1 day	Thu 7/10/14	Thu 7/10/14	260												
262	Painting	1 day	Fri 7/11/14	Fri 7/11/14	261												
263	Flooring	3 days	Mon 7/14/14	Wed 7/16/14	262												
264	Inspections	5 days	Wed 7/23/14	Tue 7/29/14	9												
265	Certificate of Occupancy	1 day	Wed 7/30/14	Wed 7/30/14	264												
266	Air Balancing	5 days	Wed 7/23/14	Tue 7/29/14	9												
267	Punchlist	5 days	Wed 7/23/14	Tue 7/29/14	9												
268	Move In	0 days	Fri 8/8/14	Fri 8/8/14													

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

April			May					June				July			August					
3/16	3/23	3/30	4/6	4/13	4/20	4/27	5/4	5/11	5/18	5/25	6/1	6/8	6/15	6/22	6/29	7/6	7/13	7/20	7/27	8/3

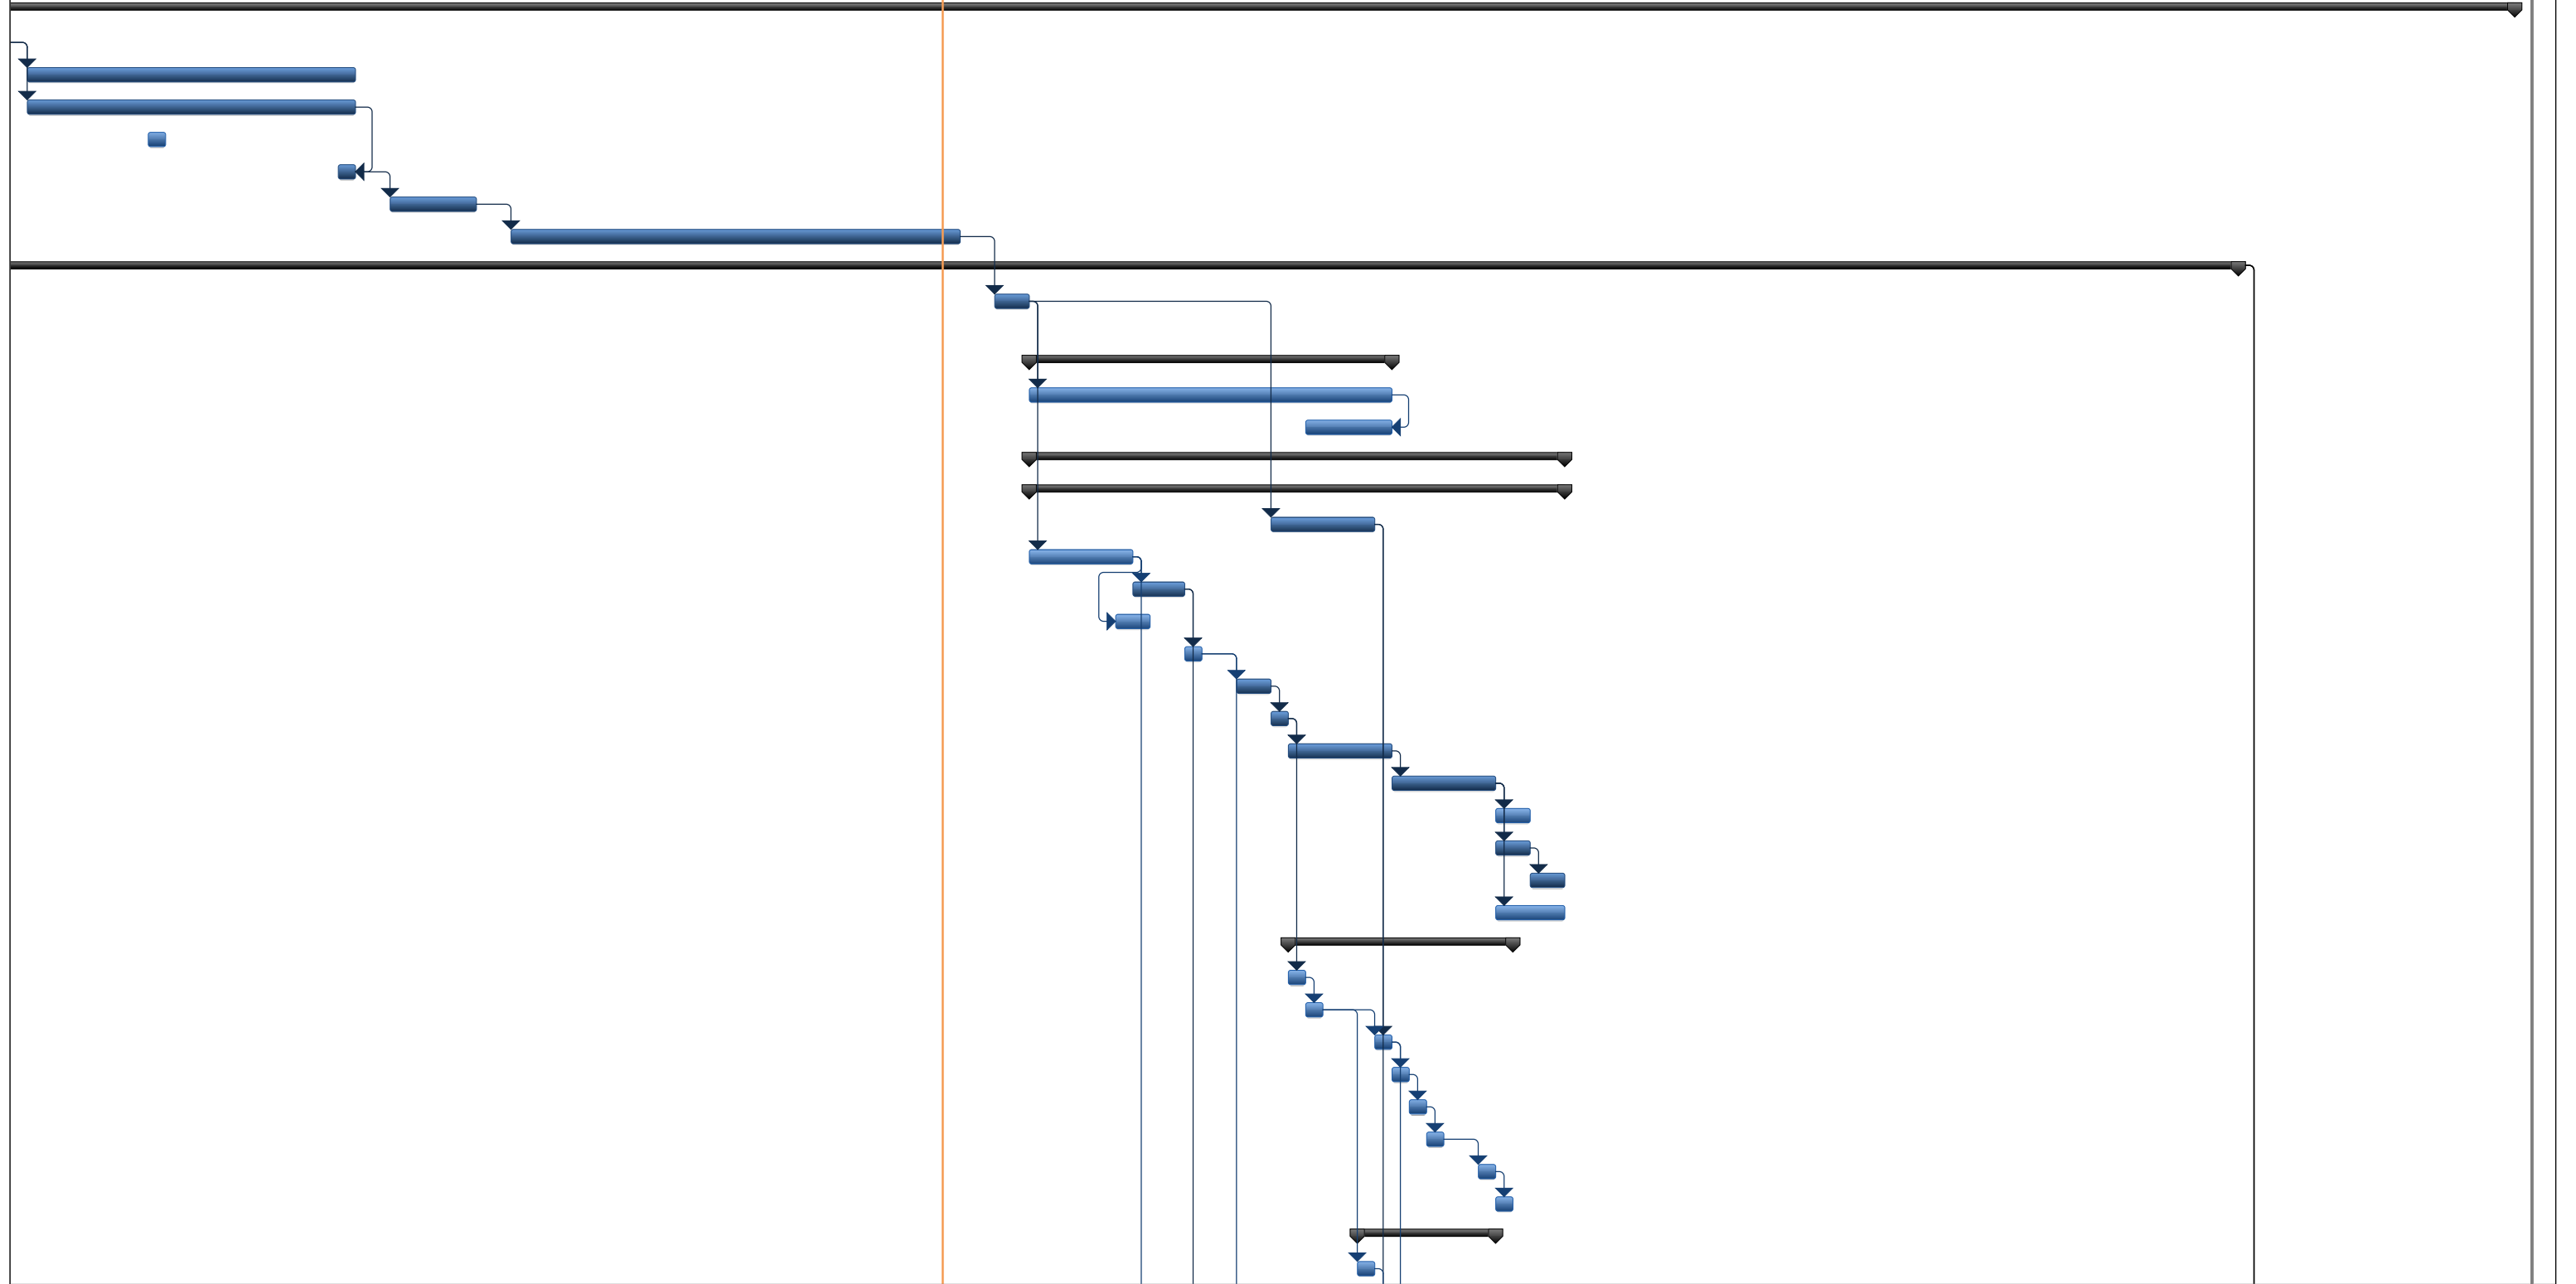


Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

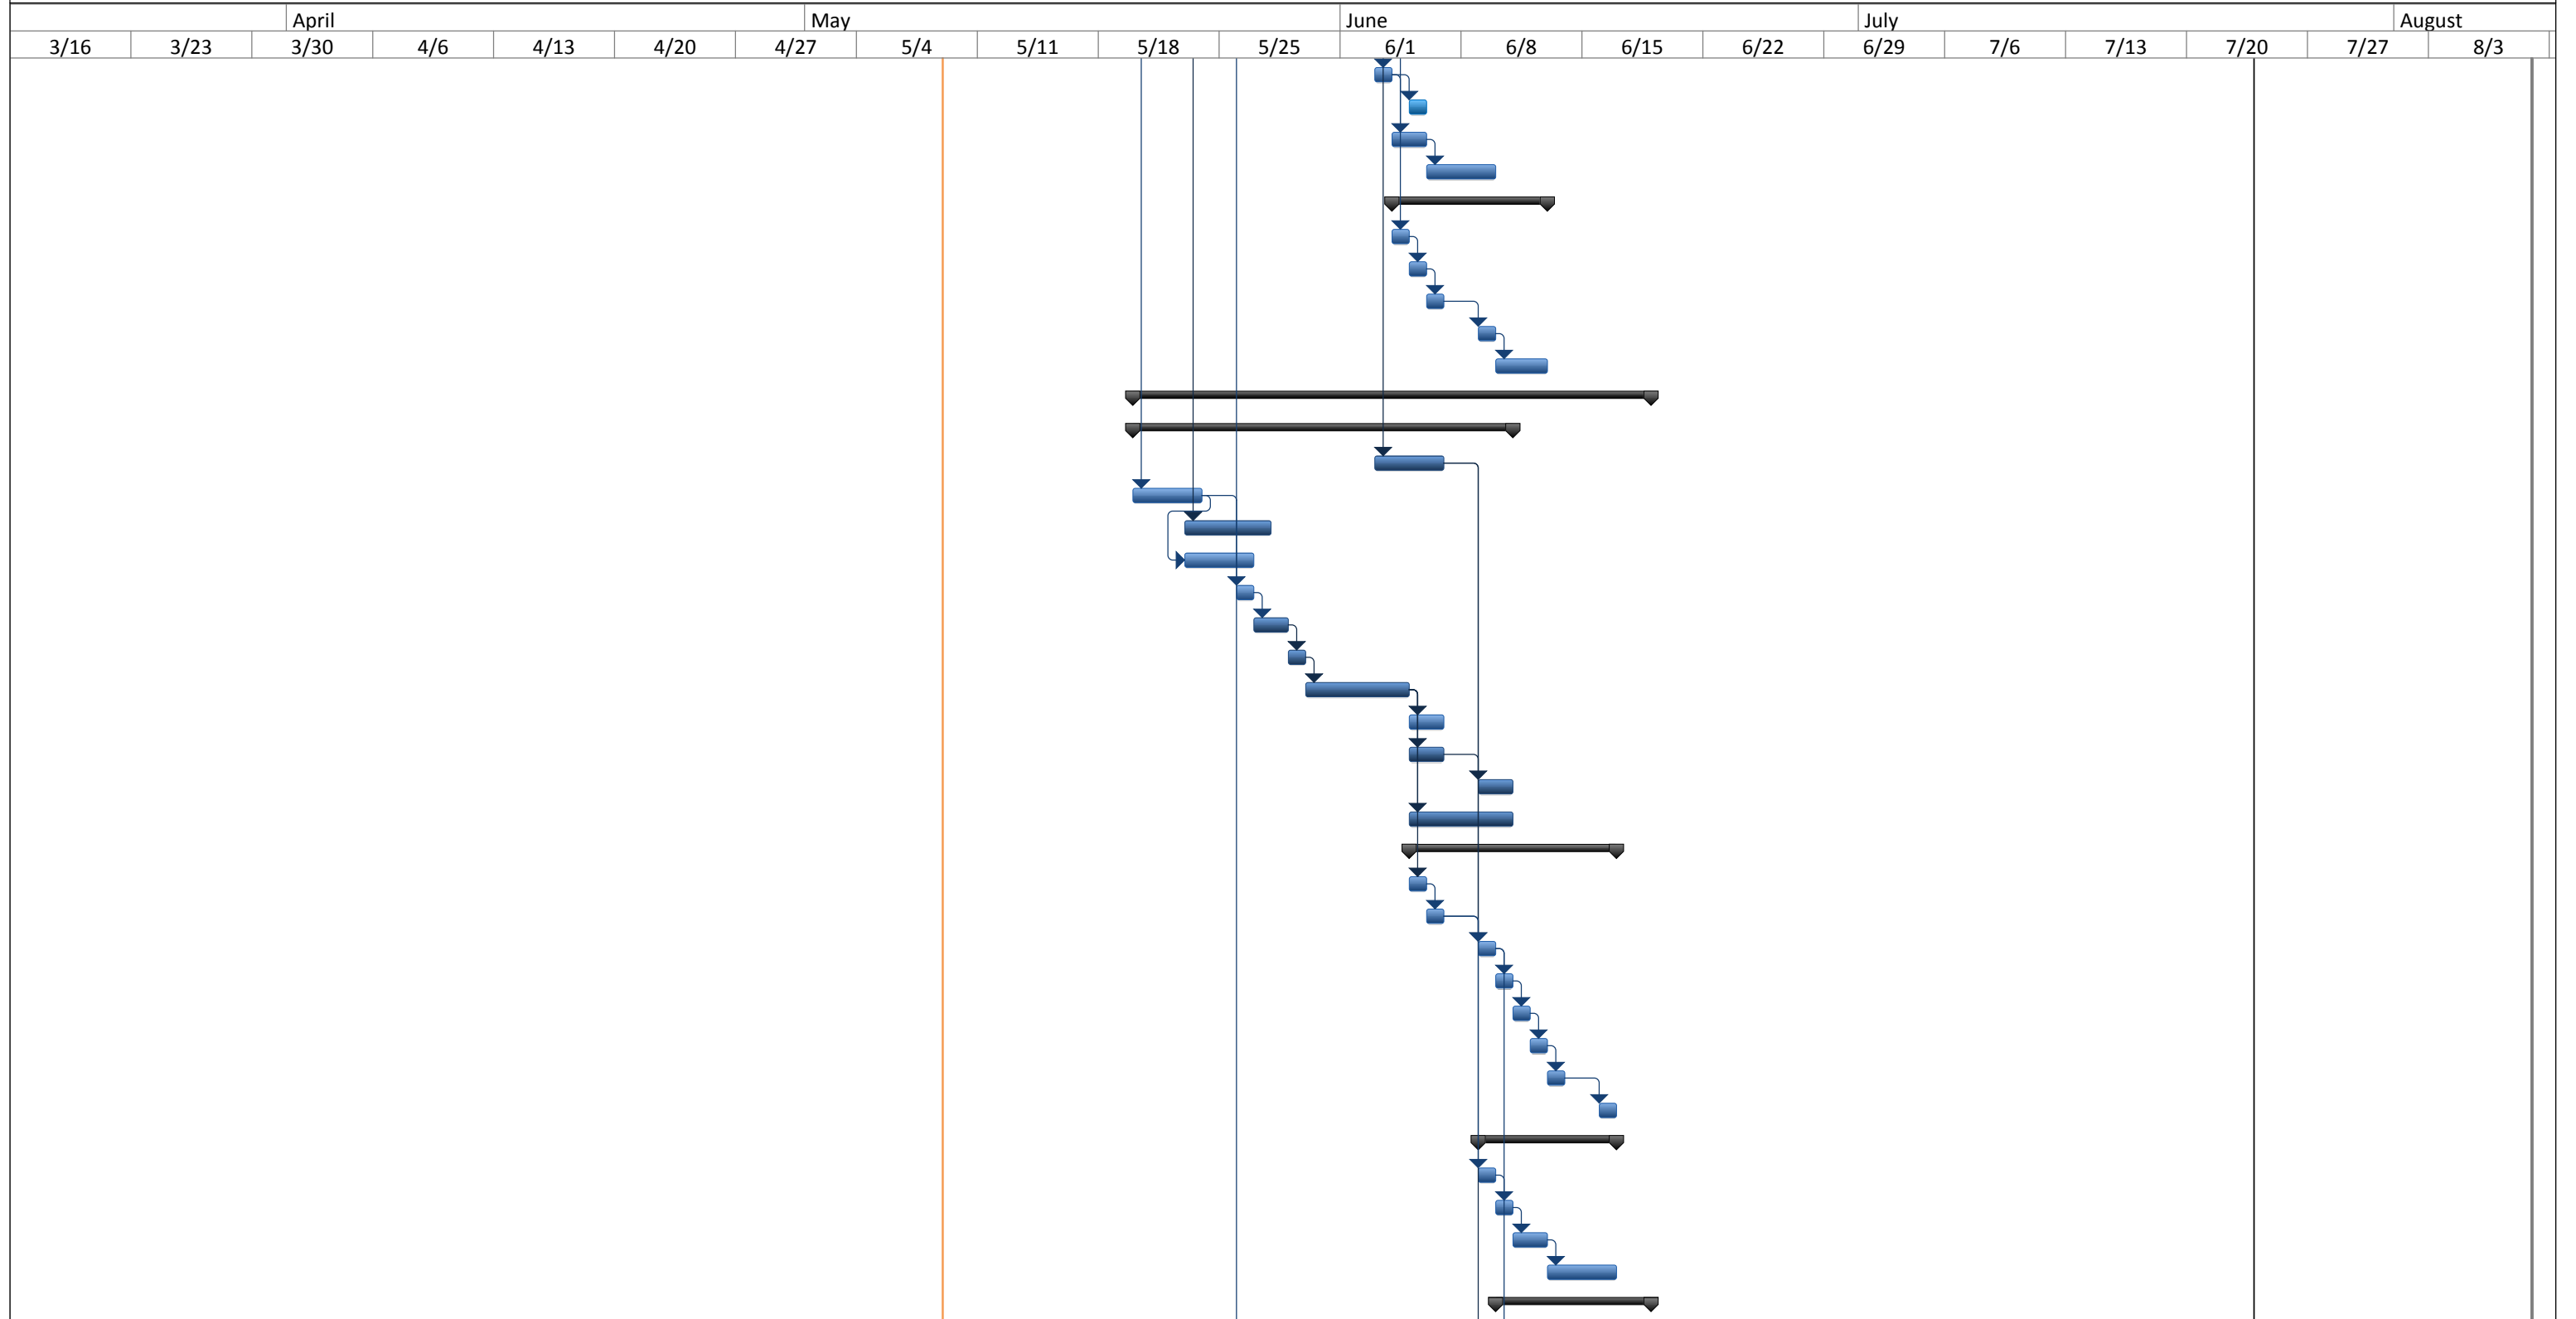

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

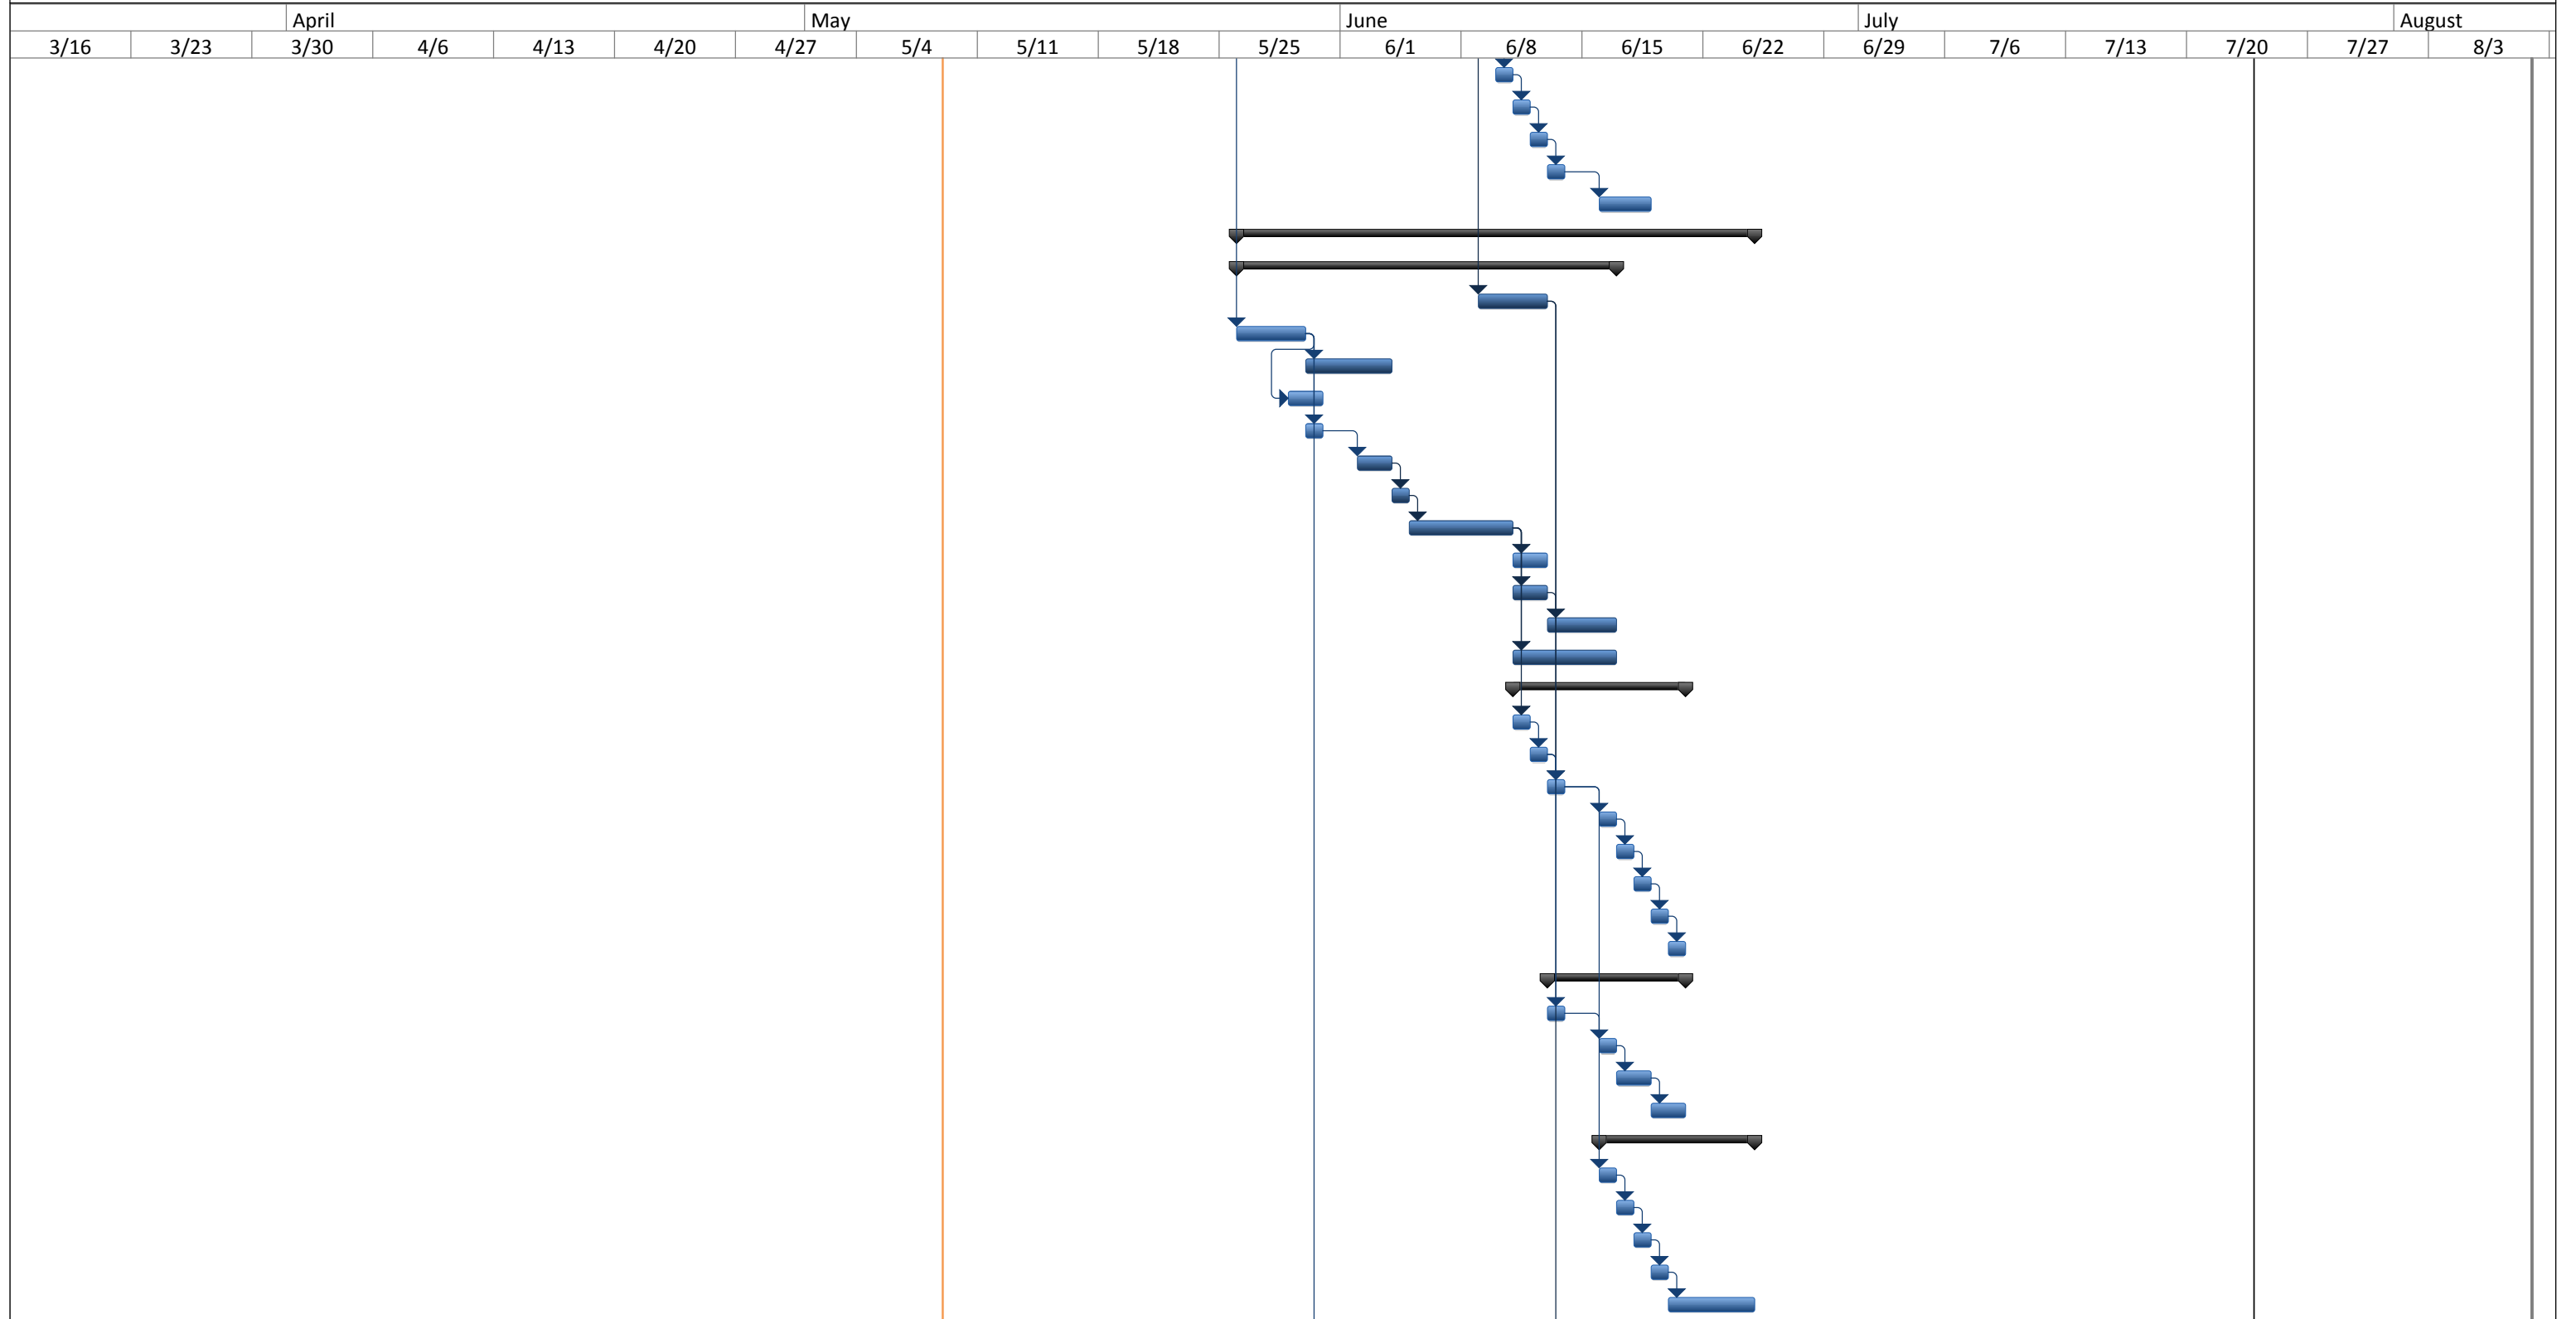

Project: Kuhlman Architectural Re
Date: 3/14/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			


KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

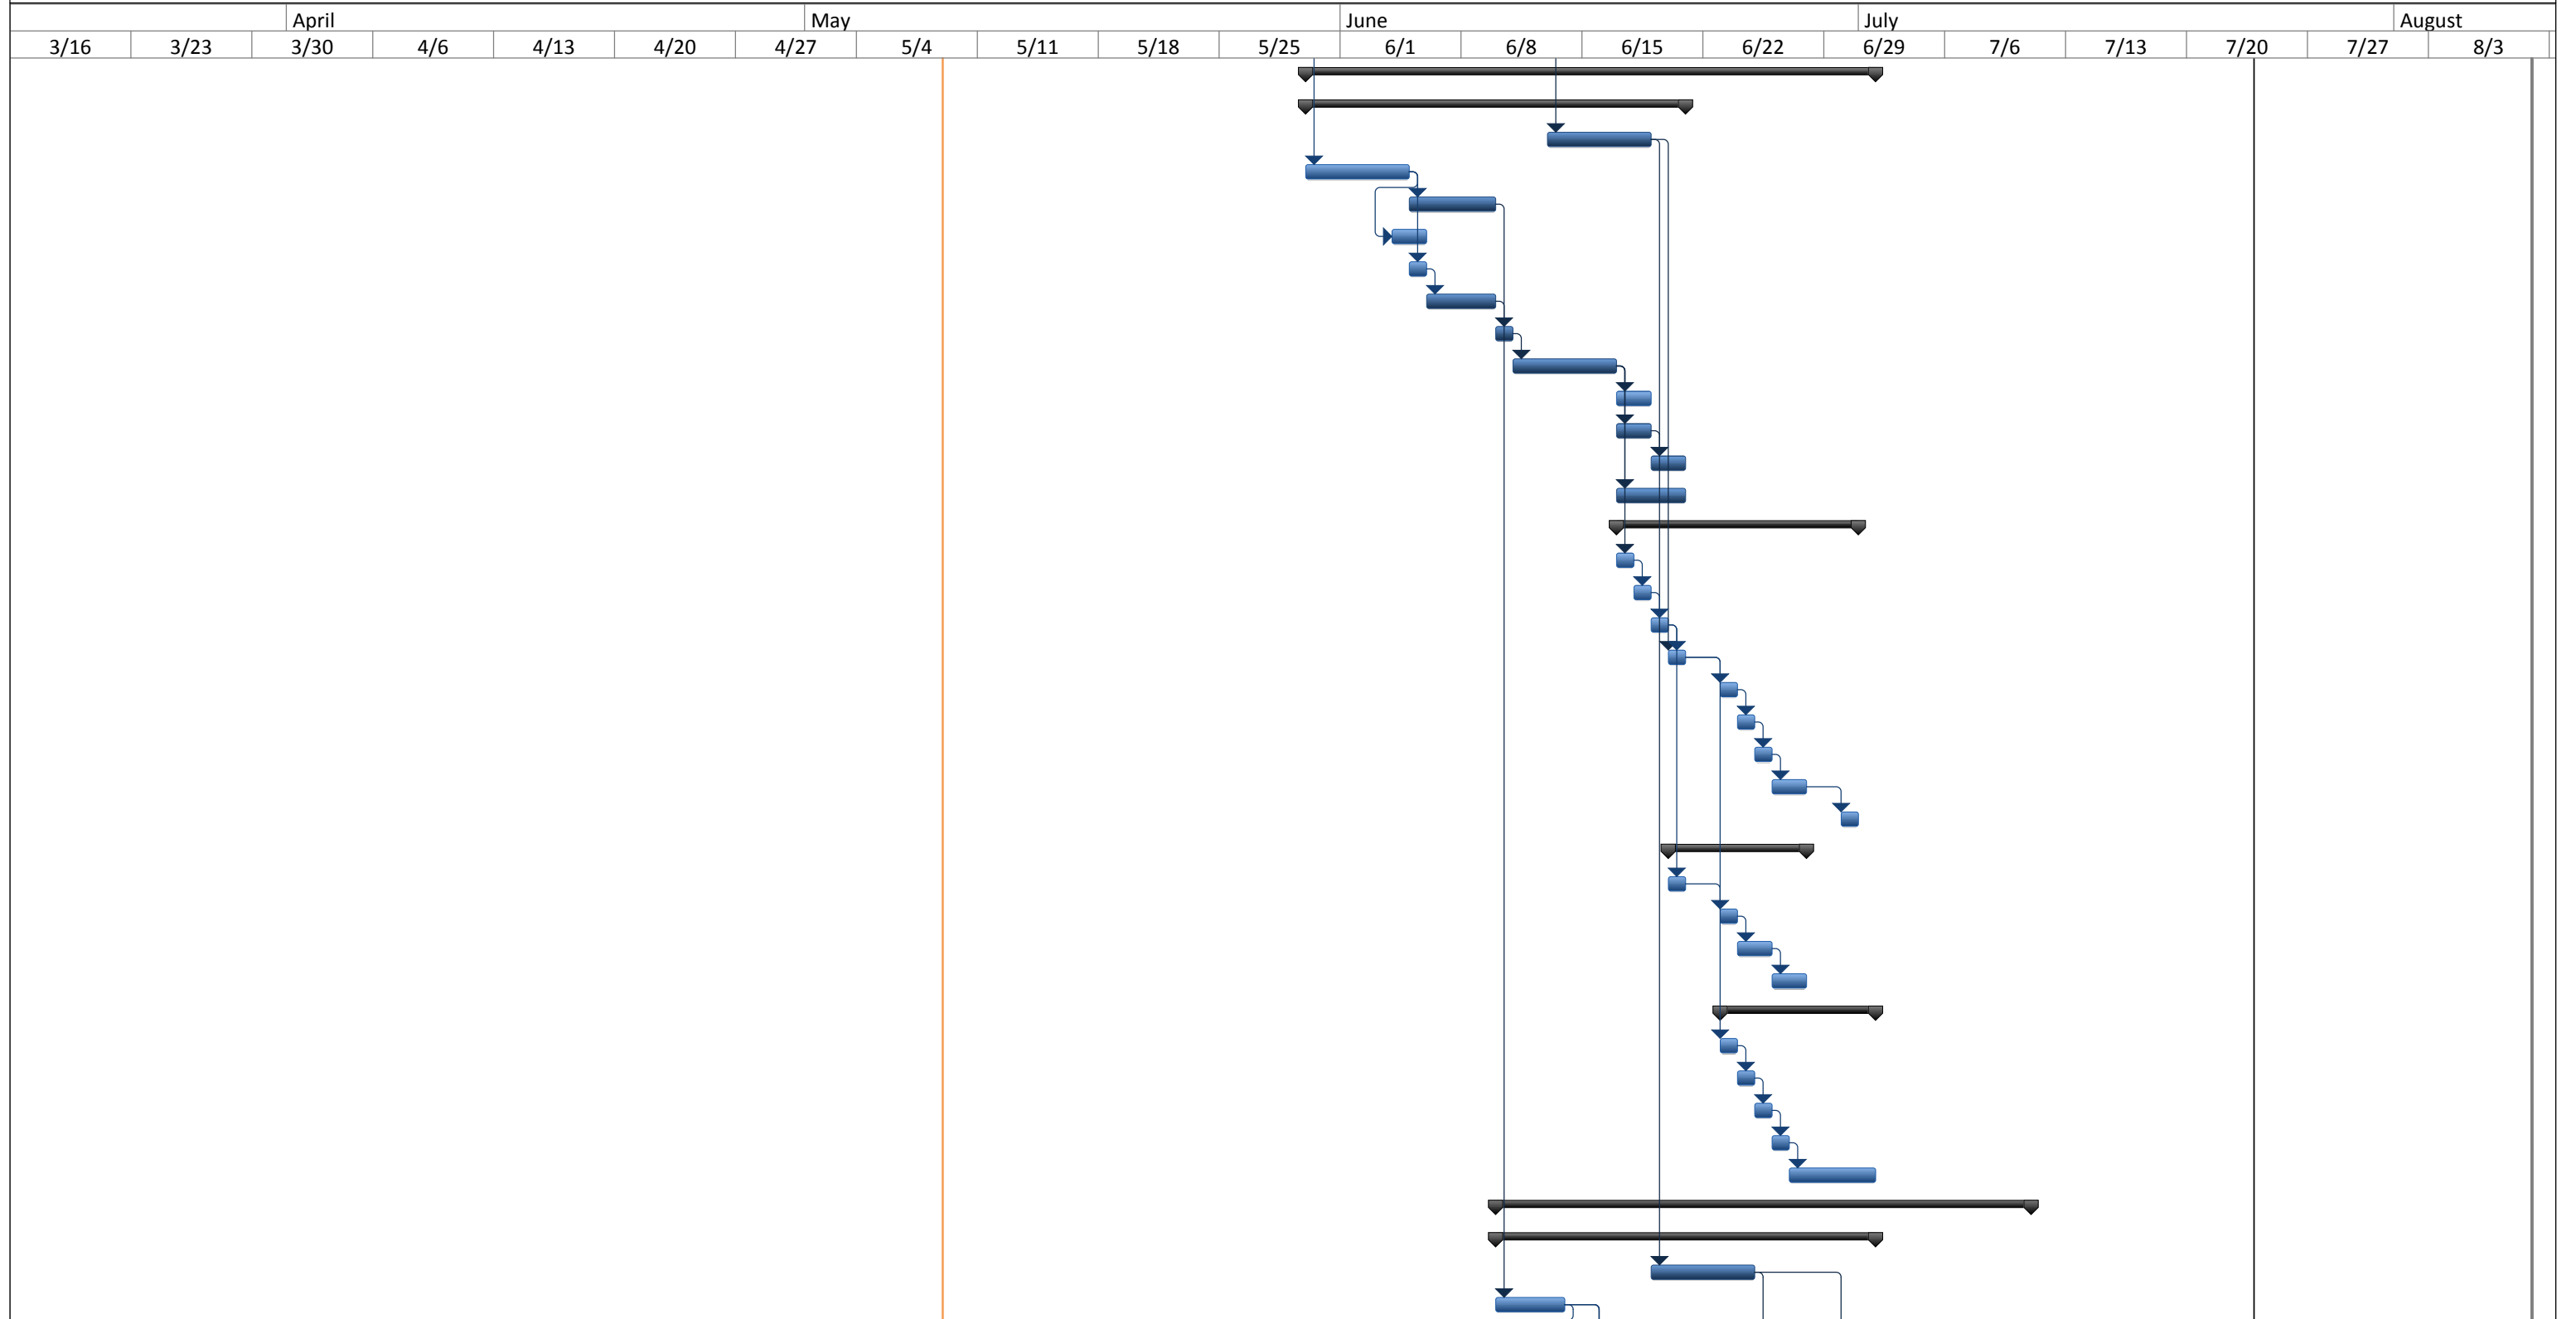

Project: Kuhlman Architectural Re
Date: 3/14/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

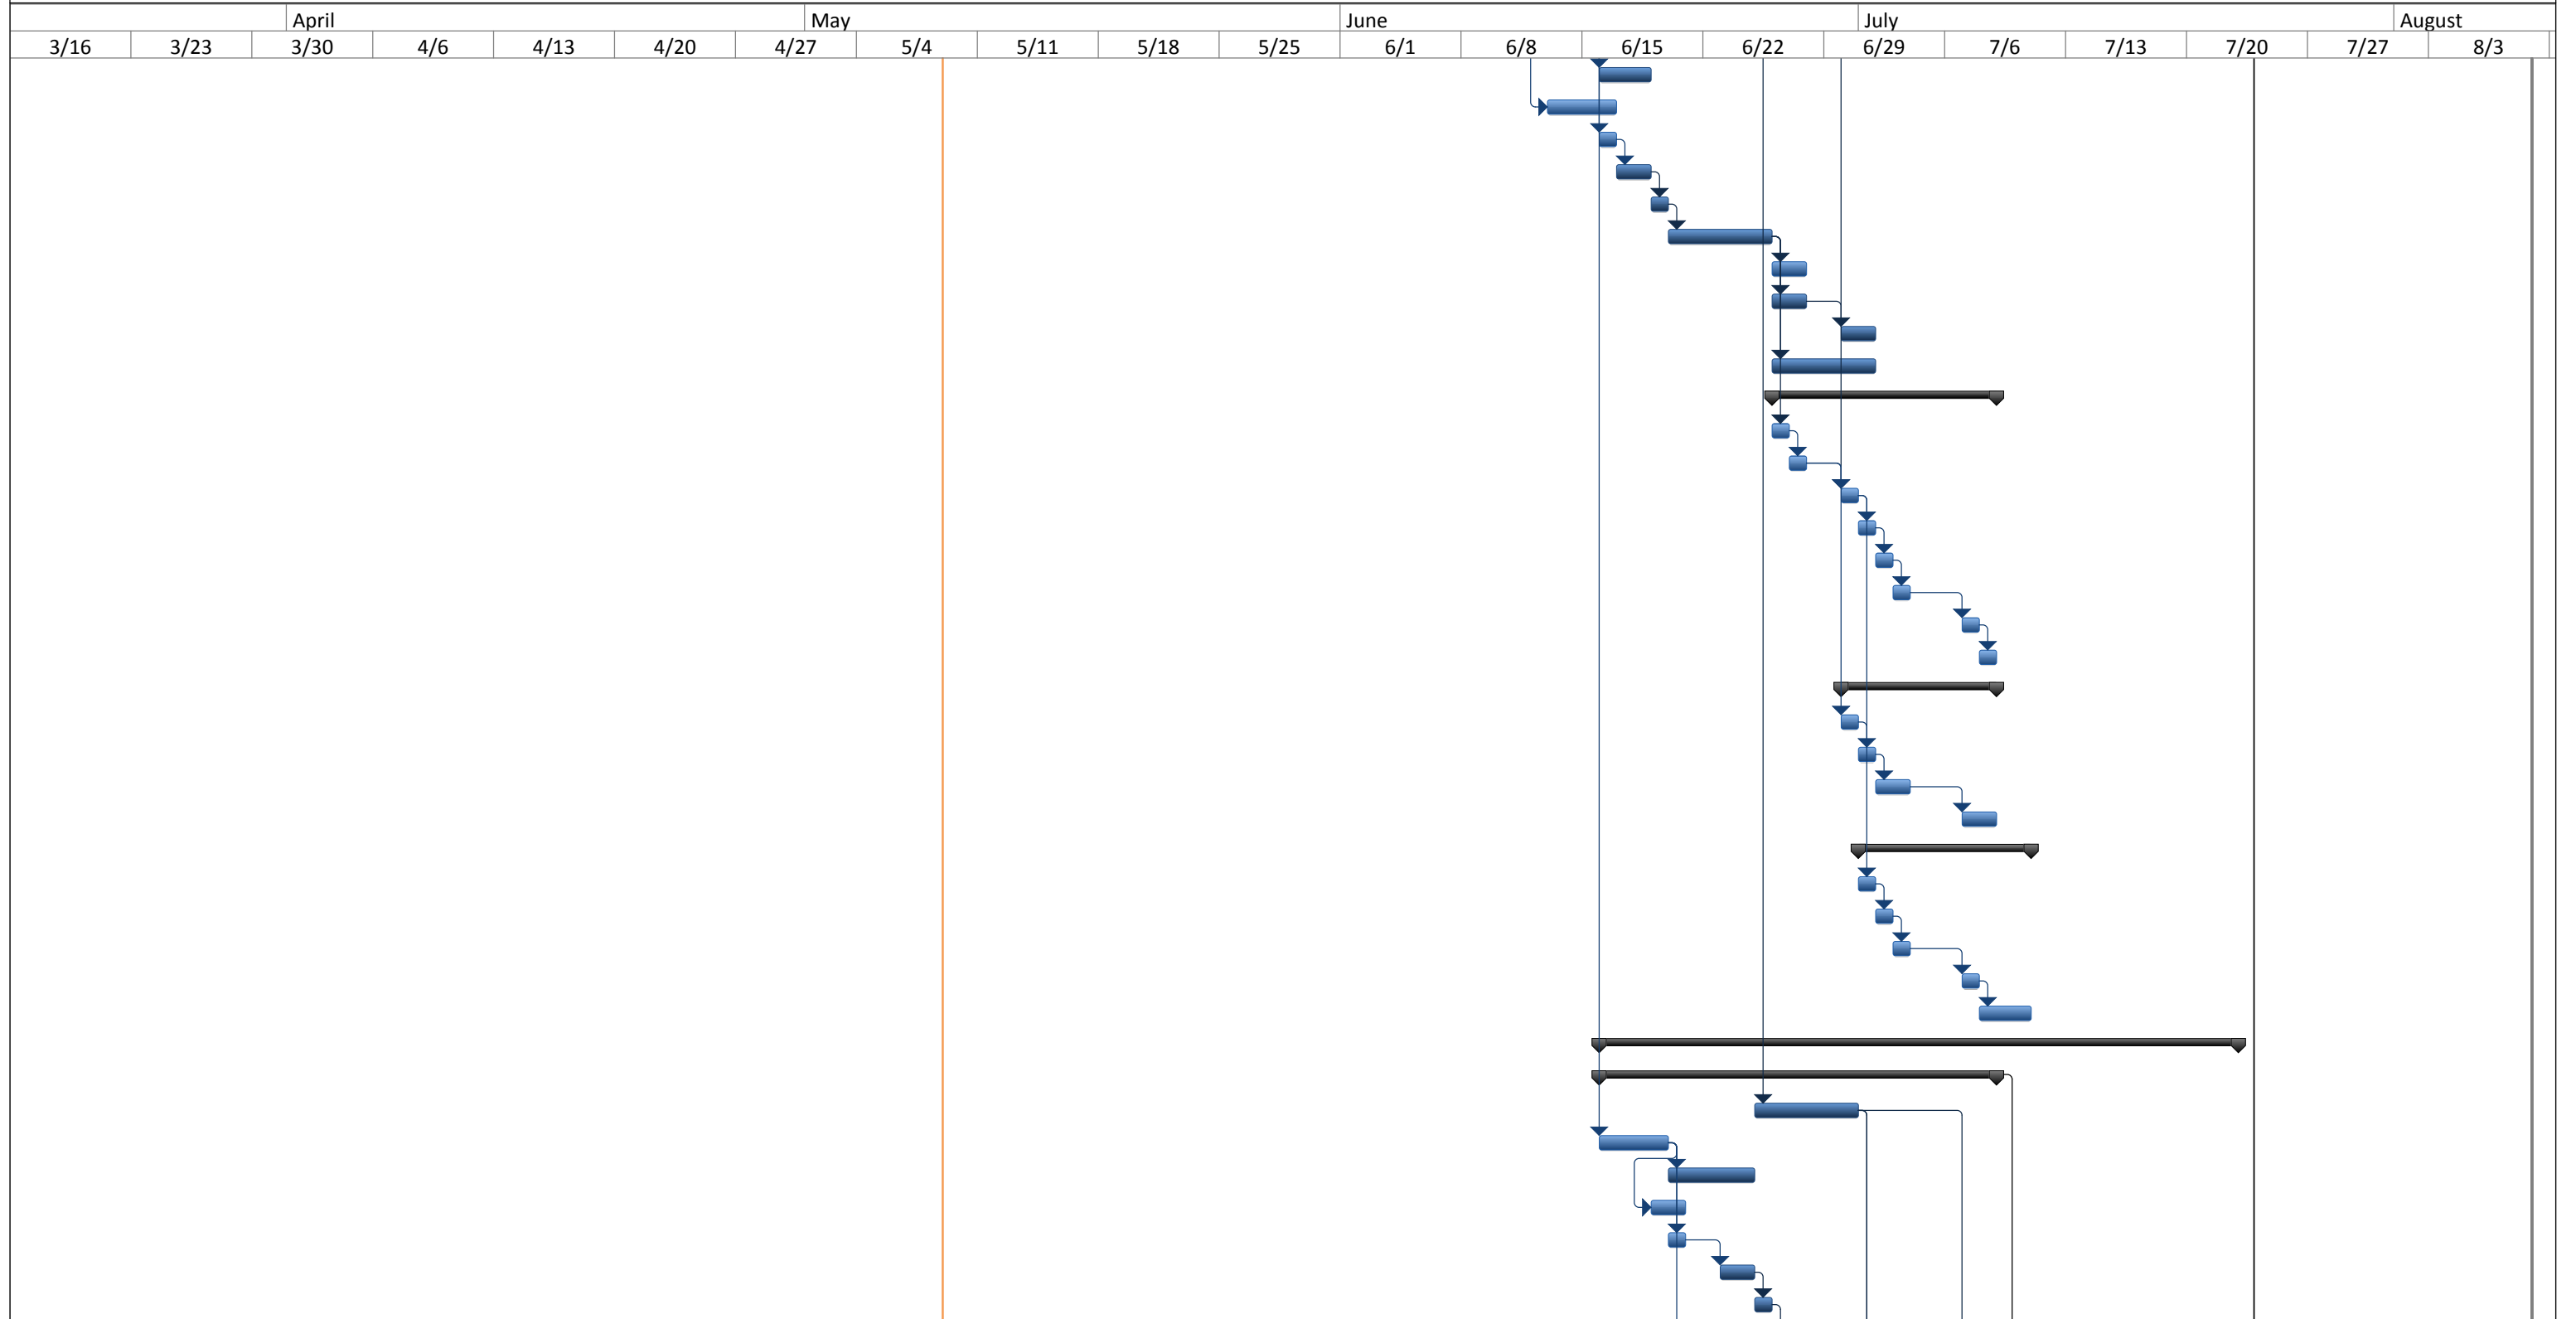


Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

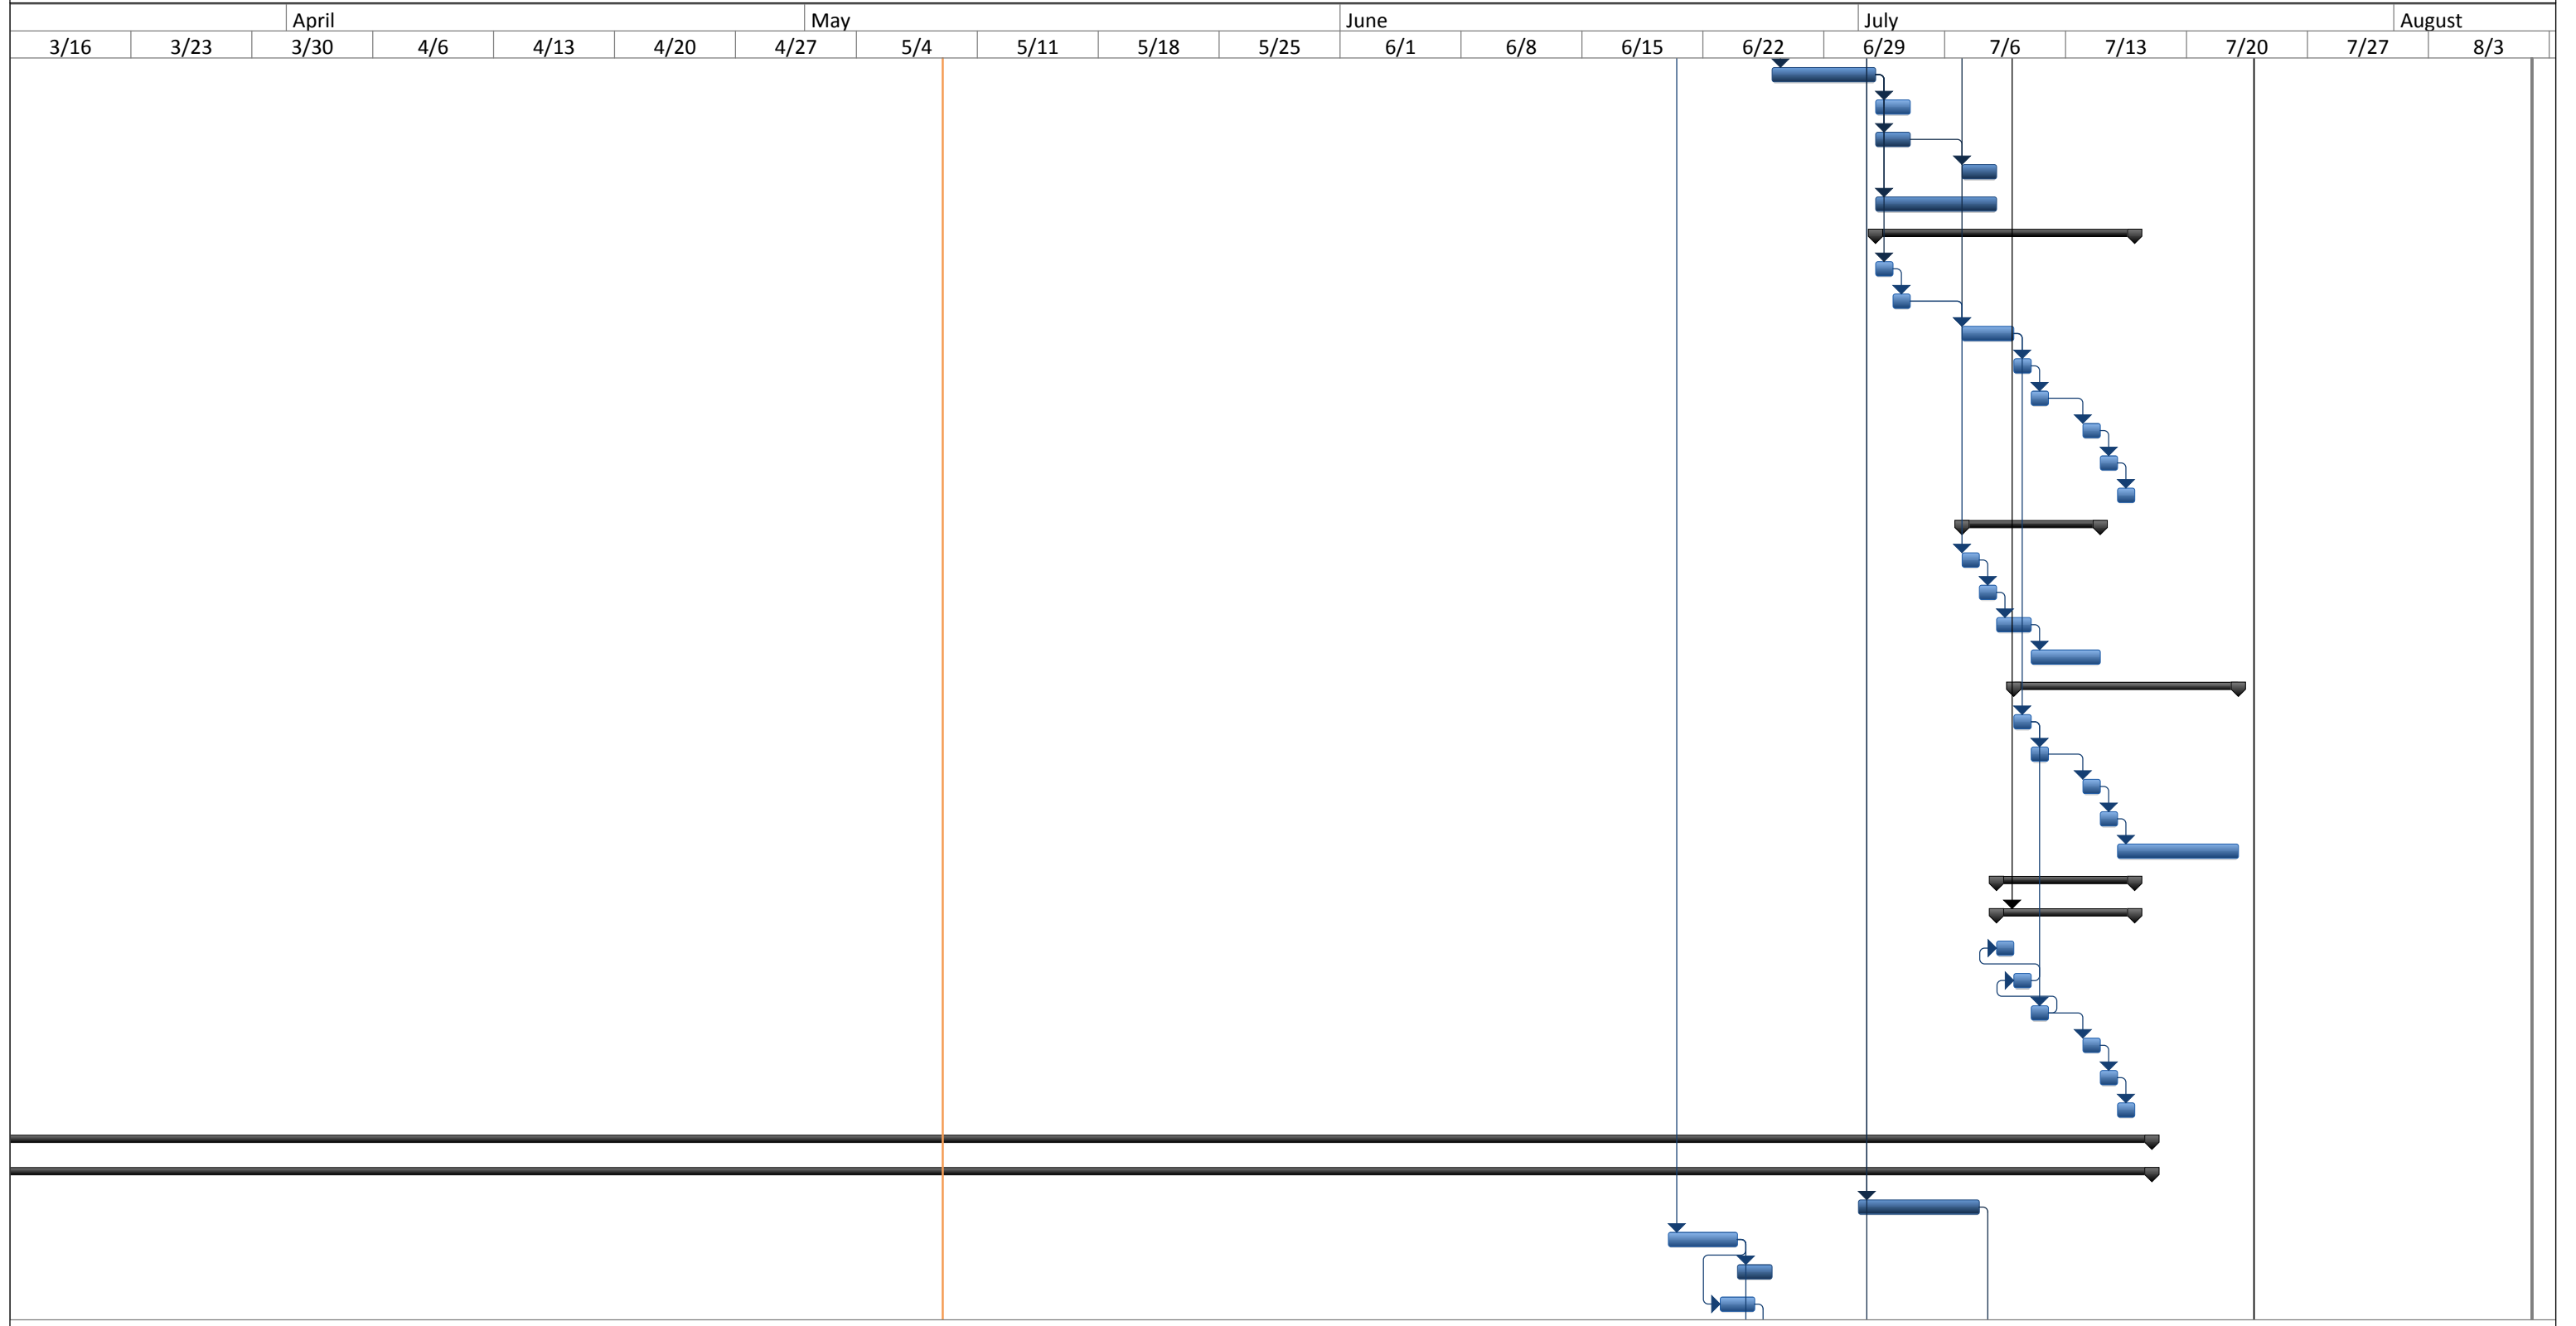

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

KUHLMAN HALL RENOVATION PHASE 2 SCHEDULE

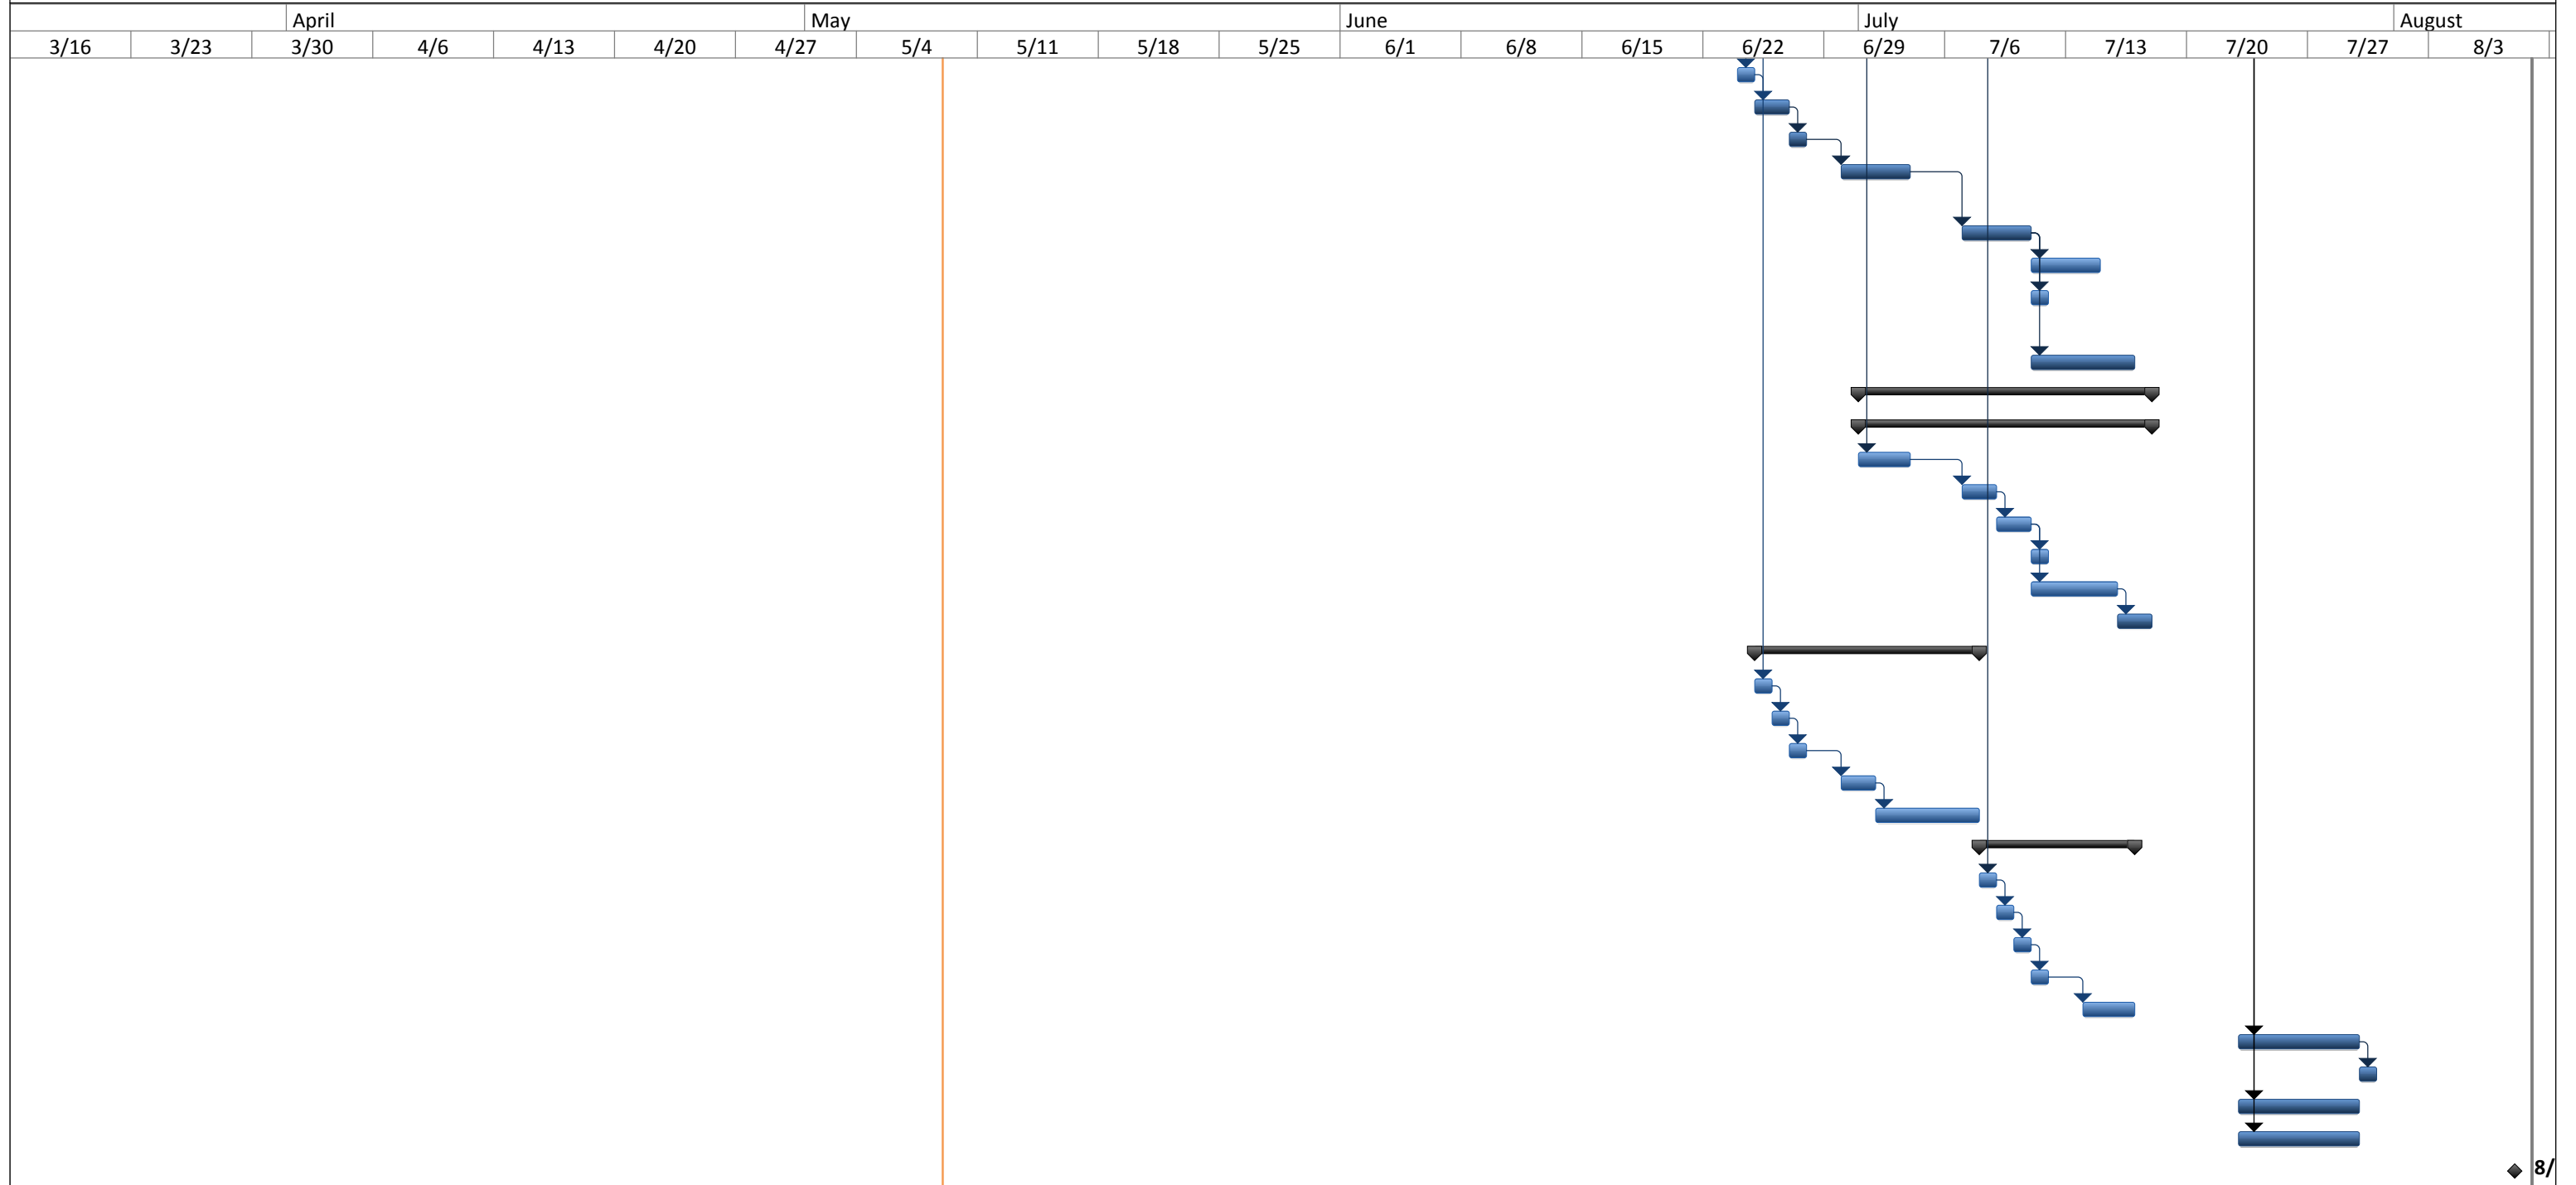

◆ 8/

Project: Kuhlman Architectural Re Date: 3/14/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
